August 15, 2016

ADDENDUM No. 1

BID DATE EXTENSION: Bid date shall be changed to 2:00 p.m. Thursday, August 25, 2016.

SIGN-IN SHEET: The attached copy of the sign-in sheet from the August 11, 2016 pre-bid walk through is provided for information only.

The following changes and/or clarifications shall be incorporated into the contract documents:

CLARIFICATIONS FROM QUESTIONS ASKED:

1. Regarding permit fees. Contrary to what may be stated in the General Conditions, all plan review and permit fees for the Building Permit from Pierce County will be paid by the owner.
2. There are at least two upper branches of an existing oak tree, directly above the building location that will need to be trimmed, as a part of the scope of the project. Contractor will need to coordinate this with the Military Department.

DRAWINGS:

CIVIL: A. No items.

ELECTRICAL:

A. Sheet E-1, revised 8-12-16, adds a 2” underground conduit for owner’s communications cabling.
B. Sheets E-2 and E-3: Added a 30A, 120V outlet that is a standard RV connection, inside the building.

SPECIFICATIONS:

A. Division 0: Substitute updated version of General Conditions, attached.
B. Table of Contents: Section 321316, change to read “Section 321313”.
C. Table of Contents: DELETE Section 321723.
D. Division 5: Section 054000, correct title should read “Cold-Formed Metal Framing”.
E. Division 7: Section 076200, 2.05A, 2: Flashings shall be 24 gauge (not 22 gauge).
F. Division 32: Section 321600, Correct title is “Curbs and Sidewalks”.

APPROVED SUBSTITUTIONS:

REJECTED SUBSTITUTIONS:

Attachments:
Attendee List.
Sheet E-1, Revised 8-12-16.
Sheets E-2 & E-3, Revised 8-15-16.

END OF ADDENDUM No. 1

© 2016

STATE OF WASHINGTON MILITARY DEPARTMENT

etal Storage BLDG 20C-Camp Murray
ate of Washington
litary Department

date: 8/11/16
location: 20C AVIATION DRIVE-Camp Murray
10:00AM Pacific

tendee	Representing	Phone(s)	email
Kevin Decker	CHET WILLIAMS CONST.	206 334 1758	kevind@chetwilliamsconstruction.com
Pete Fredrickson	WESTMARK CONSTRUCTION INC.	253-564-4620	WJOHNSON@WESTMARKCONST.COM
Troy Williams	Chet Williams Const Inc.	206-713-0694	troyw@chetwilliams Construction
Darell Waterman	Hi Mark Construction	253-377-4595	dwh20man@msn.com
Ryan Covington	Allen-Bradbury Construction	253-218-2288	ryan@allenbradburyconstruction.com

Instructions to Bidders - July 2016
General Conditions - July 2010
Supplemental Conditions - July 2016

For State Facility Construction

Effective: July 1, 2016

Approved by:

William J. Frare, Assistant Director
Engineering and Architectural Services

Dawn Cortez, Assistant Attorney General
Washington State Office of the Attorney General

Washington State Department of
Enterprise Services
Facilities Division, Engineering and Architectural Services
P.O. Box 41476
Olympia, Washington 98504-1476
360.902.7272

INSTRUCTIONS TO BIDDERS
FOR WASHINGTON STATE FACILITIES CONSTRUCTION

PART 0 – GENERAL CONDITIONS

1.1 EXPLANATION TO PROSPECTIVE BIDDERS

A. In accordance with RCW 39.04.380 effective *March 30, 2012* the State of Washington is enforcing a **Reciprocal Preference for Resident Contractors**. Any public works bid received from a nonresident contractor from a state that provides an in-state percentage bidding preference, a comparable percentage disadvantage must be applied to the bid of that nonresident contractor.

A nonresident contractor from a state that provides a percentage bid preference means a contractor that:

a) is from a state that provides a percentage bid preference to its resident contractors bidding on public works contracts.
b) at the time of bidding on a public works project, does not have a physical office located in Washington.

The state of residence for a nonresident contractor is the state in which the contractor was incorporated or, if not a corporation, the state where the contractor's business entity was formed.

All nonresident contractors will be evaluated for out of state bidder preference. If the state of the nonresident contractor provides an in-state contractor preference, a comparable percentage disadvantage will be applied to their bid prior to contract award.

This section does not apply to public works procured pursuant to RCW 39.04.155, 39.04.280, or any other procurement exempt from competitive bidding.

B. Any prospective bidder desiring an explanation or interpretation of the solicitation, drawings, specifications, etc., must submit a request in writing to the Architect/Engineer (A/E) seven (7) calendar days before the bid due date. Oral explanations or instructions given before the award of a contract will not be binding. Any information given a prospective bidder concerning a solicitation will be furnished promptly to all other prospective bidders by addendum to the solicitation, if that information is necessary in submitting bids or if the lack of it would be prejudicial to other prospective bidders.

C. In accordance with the legislative findings and policies set forth in Chapter 39.19 RCW the State of Washington encourages participation in all of its contracts by MWBE firms certified by the Office of Minority and Women's Business Enterprises (OMWBE). Participation may be either on a direct basis in response to this invitation

or as a subcontractor to a bidder. However, unless required by federal statutes, regulations, grants, or contract terms referenced in the contract documents, no preference will be included in the evaluation of bids, no minimum level of MWBE participation shall be required as a condition for receiving an award, and bids will not be rejected or considered non-responsive on that basis. Any affirmative action requirements set forth in federal regulations or statutes included or referenced in the contract documents will apply.

D. The State of Washington encourages participation in all of its contracts by Veteran-owned businesses (defined in RCW 43.60.010) and located at http://www.dva.wa.gov/program/certified-veteran-and-servicemember-owned-businesses and Small, Mini and Micro businesses (defined in RCW 39.26.010) which have registered in WEBS at https://fortress.wa.gov/ga/webs/.

1. In order to report payment detail, the Contractor must create an account with the DES Diversity Compliance program (B2Gnow) or verify if an account has already been created on behalf of the Contractor: https://des.diversitycompliance.com. B2Gnow is designed to streamline and automate compliance reporting requirements, empowering vendors to maintain accurate contact information and submit contract payment details online.

2. For account login or account creation details, please refer to the Quick Reference Guides located on pages 4 - 6 or go to B2Gnow home page by clicking on the URL listed above and clicking on the "Help/First Time Users" link.

3. Every month for the duration of your contract, submit the following payment information through B2Gnow:
   a. Payments received by the prime contractor from the Agency
   b. Payments paid to each subcontractor, including lower tier subcontractors
   c. Payments paid to each supplier

E. In accordance with RCW 39.04.320 the state of Washington requires 15% **Apprenticeship Participation** for all projects estimated to cost one million dollars or more. On applicable projects the bid advertisement and Bid Proposal form shall establish a minimum required percentage of apprentice labor hours compared to the total labor hours. Bidders may contact the Department of Labor and Industries, Specialty Compliance Services Division, Apprenticeship Section, P.O. Box 44530, Olympia, WA 98504-4530, by phone (360) 902-5320, and e-mail at Apprentice@lni.wa.gov, to obtain information on available apprenticeship programs.

1.2 PREPARATION OF BIDS – CONSTRUCTION

A. Bids must be: (1) submitted on the bid proposal forms, or copies of forms, furnished by the Owner or the Owner's agent, and (2) signed in ink. The person signing a bid must

initial each change appearing on any bid form. If the bid is made by a corporation, it shall be signed by the corporation's authorized designee. The address of the bidder shall be typed or printed on the bid form in the space provided.

B. The bid form may require bidders to submit bid prices for one or more items on various bases, including: (1) lump sum base bid; (2) lump sum bid alternate prices; (3) unit prices; or (4) any combination of items 1 through 3 above.

C. If the solicitation includes alternate bid items, failure to bid on the alternates may disqualify the bid. If bidding on all items is not required, bidders should insert the words "no bid" in the space provided for any item on which no price is submitted.

D. Substitute bid proposals will not be considered unless this solicitation authorizes their submission.

1.3 BID GUARANTEE

A. When the sum of the base bid plus all additive bid alternates is $35,000.00 or less, bid security is not required.

When the sum of the base bid plus all additive alternates is greater than $35,000.00, a bid guarantee in the amount of 5% of the base bid amount is required. Failure of the bidder to provide bid guarantee when required shall render the bid non-responsive.

B. Acceptable forms of bid guarantee are: A bid bond or postal money order, or certified check or cashier's check made payable to the Washington State Treasurer.

The Owner will return bid guarantees (other than bid bond) to unsuccessful bidders as soon as practicable, but not sooner than the execution of a contract with the successful bidder. The successful bidder's bid guarantee will be returned to the successful bidder with its official notice to proceed with the work of the contract.

C. The bidder will allow 60 days from bid opening date for acceptance of its bid by the Owner.

The bidder will return to the Owner a signed contract, insurance certificate and bond or bond waiver within 15 days after receipt of the contract. If the apparent successful bidder fails to sign all contractual documents or provide the bond and insurance as required or return the documents within 15 days after receipt of the contract, the Owner may terminate the award of the contract.

D. In the event a bidder discovers an error in its bid following the bid opening, the bidder may request to withdraw its bid under the following conditions:

1. Written notification is received by the Owner within 24 hours following bid opening.

2. The bidder provides written documentation of the claimed error to the satisfaction of the Owner within 72 hours following the bid opening.

   The Owner will approve or disapprove the request for withdrawal of the bid in writing. If the bidder's request for withdrawal of its bid is approved, the bidder will be released from further obligation to the Owner without penalty. If it is disapproved, the Owner may retain the bidder's bid guarantee.

1.4 ADDITIVE OR DEDUCTIVE BID ITEMS

The low bidder, for purposes of award, shall be the responsive bidder offering the low aggregate amount for the base bid item, plus additive or deductive bid alternates selected by the Owner, and within funds available for the project.

The bidder agrees to hold all bid alternate prices for sixty (60) days from date of bid opening.

1.5 ACKNOWLEDGEMENT OF ADDENDA

Bidders shall acknowledge receipt of all addenda to this solicitation by identifying the addenda numbers in the space provided for this purpose on the bid proposal form. Failure to do so may result in the bid being declared non-responsive.

1.6 SITE INVESTIGATION AND CONDITIONS AFFECTING THE WORK

The bidder acknowledges that it has taken steps necessary to ascertain the nature and location of the work, and that it has investigated and satisfied itself as to the general and local conditions which can affect the work or its cost, including but not limited to (1) conditions bearing upon transportation, disposal, handling, and storage of materials; (2) the availability of labor, water, electric power, and road; (3) uncertainties of weather, river stages, tides, or similar physical conditions at the site; (4) the conformation and conditions of the ground; and (5) the character of equipment and facilities needed preliminary to and during the work. The bidder also acknowledges that it has satisfied itself as to character, quality, and quantity of surface and subsurface materials or obstacles to be encountered insofar as this information is reasonably ascertainable from an inspection of the site, including exploratory work done by the Owner, as well as from the drawings and specifications made a part of this contract. Any failure of the bidder to take the actions described and acknowledged in this paragraph will not relieve the bidder from responsibility for estimating properly the difficulty and cost of successfully performing the work.

1.7 BID AMOUNTS

A. The bid prices shown for each item on the bid proposal shall include all labor, material, equipment, overhead and compensation to complete all of the work for that item.

B. The actual cost of building permit (only) and the public utility hookup fees will be a direct reimbursement to the Contractor or paid directly to the permitting agency by the Owner. Fees for these permits should not be included by the Bidder in the bid amount.

C. The Bidder agrees to hold the base bid prices for sixty (60) days from date of bid opening.

1.8 TAXES

The bid amounts shall not include Washington State Sales Tax (WSST). All other taxes imposed by law shall be included in the bid amount. The Owner will include WSST in progress payments. The Contractor shall pay the WSST to the Department of Revenue and shall furnish proof of payment to the Owner if requested.

[NOTE: Contractor must bond for contract amount plus the WSST.]

1.9 SUBMISSION OF BIDS

A. Bid Proposals must be submitted on or before the time specified in the Advertisement for Bids.

B. If the base bid and the sum of the additive alternates is one million dollars or more, the Bid Proposal shall comply with the following requirements:

1. Pursuant to RCW 39.30.060, if the base bid and the sum of the additive alternates is one million dollars or more, the Bidder shall provide names of the Subcontractors with whom the Bidder will subcontract for performance of heating, ventilation and air conditioning (HVAC), plumbing, and electrical.

2. The Bidder can name itself for the performance of the work.

3. The Bidder shall not list more than one Subcontractor for each category of work identified UNLESS Subcontractors vary with bid alternates, in which case the Bidder must indicate which Subcontractor will be used for which alternate.

4. Failure of the Bidder to submit as part of the bid the NAMES of such Subcontractors or to name itself to perform such work shall render the Bidder's bid nonresponsive and, therefore, void.

C. The Bid Proposal shall be submitted in a sealed envelope addressed to the office specified in the Advertisement for Bids. The envelope shall have printed on the outside:

1. The project number and description.
2. The name and address of the bidder.

3. Identification as Bid Proposal.

D. Prior to the bid opening, the Owner's representative will designate the official bid clock. Any part of the bid proposal or bid modification not received prior to the times specified, per the designated bid clock, will not be considered and the bid will be returned to the bidder unopened.

E. A bid may be withdrawn in person by a bidder's authorized representative before the opening of the bids. Bidder(s) representative will be required to show ID and sign on bid summary sheet before it will be released.

F. People with disabilities who wish to request special accommodation, (e.g., sign language interpreters, Braille, etc.) need to contact the Owner ten (10) working days prior to the scheduled bid opening.

1.10 BID RESULTS

After the Bid Opening, Bidders may obtain bid results by logging on to the Military Department's web site: https://mil.wa.gov/contracts/public-works. Bid results may also be obtained from the A/E.

1.11 LOW RESPONSIBLE BIDDER

A. **Mandatory Responsibility Criteria**: Before award of a public works contract, a bidder must meet the following mandatory responsibility criteria under RCW 39.04.350 (1) to be considered a responsible bidder and qualified to be awarded a public works project. The bidder must:

1. At the time of bid submittal, have a certificate of registration in compliance with chapter 18.27 RCW;

2. Have a current state unified business identifier number;

3. If applicable, have industrial insurance coverage for the bidder's employees working in Washington as required in Title 51 RCW; an employment security department number as required in Title 50 RCW; and a state excise tax registration number as required in Title 82 RCW;

4. Not be disqualified from bidding on any public works contract under RCW 39.06.010 or 39.12.065(3); and

5. If bidding on a public works project subject to the apprenticeship utilization requirements in RCW 39.04.320, not have been found out of compliance by the Washington state apprenticeship and training council for working apprentices out of ratio, without appropriate supervision, or outside their approved work

processes as outlined in their standards of apprenticeship under chapter 49.04 RCW for the one-year period immediately preceding the date of the bid solicitation.

6. Until December 31, 2013, not have violated the "Off-site Prefabrication" reporting requirement more than one time as determined by the Department of Labor and Industries.

B. **Supplemental Responsibility Criteria:** In addition to the mandatory bidder responsibility, the Owner may adopt relevant supplemental criteria for determining bidder responsibility applicable to a particular project which the bidder must meet (RCW 39.04.350 (2)).

1. If applicable, the Owner shall consider an overall accounting of the attached supplemental criteria for determining bidder responsibility "DIVISION 00 RESPONSIBILITY CRITERIA"**.**

2. At least seven (7) days prior to the bid submittal deadline, a potential bidder may request that the Owner modify the supplemental responsibility criteria. The Owner will evaluate the information submitted by the potential bidder and respond before the bid submittal deadline. If the evaluation results in a change of the criteria, the Owner will issue an addendum to the bidding documents identifying the new criteria.

3. Upon Owner's request, the apparent low bidder must supply the requested responsibility information within two (2) business days of request by Owner. Withholding information or failure to submit all the information requested within the time provided may render the bid non-responsive.

4. If the Owner determines that the apparent low bidder is not responsible, the Owner will notify the bidder of its preliminary determination in writing.

5. Within three (3) days after receipt of the preliminary determination, the bidder may withdraw its bid or request a hearing where the bidder may appeal the preliminary determination and present additional information to the Owner.

6. The Owner will schedule a hearing within three (3) working days of receipt of the bidder's request. The hearing members will include a Client Agency Representative, EAS Assistant Director or designee, Deputy Assistant Director or designee, and Project Manager.

7. The Owner will issue a Final Determination after reviewing information presented at the hearing.

8. If the Owner determines a bidder to be not responsible, the Owner will provide, in writing, the reasons for the determination. If the final determination affirms that

the bidder is not responsible, the Owner will not execute a contract with any other bidder until two (2) business days after the bidder determined to be not responsible has received the final determination.

9. The Owner's Final Determination is specific to this project, and will have no effect on other or future projects.

1.12 CONTRACT AWARD

A. The Owner will evaluate bids responsiveness and responsibility.

1. A bid will be considered responsive if it meets the following requirements:

   a) It is received at the proper time and place.
   b) It meets the stated requirements of the bid proposal.
   c) It is submitted by a licensed/registered contractor within the state of Washington at the time of bid opening and is not banned from bidding by the Department of Labor and Industries.
   d) It is accompanied by a bid guarantee, if required.

2. A bid will be considered responsible if it meets the following requirements:

   a) It meets the mandatory responsibility criteria established in RCW 39.04.350 and an overall accounting of the supplemental responsibility criteria established for the project.

B. The Owner reserves the right to accept or reject any or all bid proposals and to waive informalities.

C. The Owner may negotiate bid price adjustments with the low responsive bidder, including changes in the contract documents, to bring the bid within the available funding per RCW 39.04.015.

D. The apparent low bidder, for purpose of award, shall be the responsive and responsible bidder offering the low aggregate amount for the base bid plus selected additive or deductive bid alternates and meeting all other bid submittal requirements.

E. **Reciprocal Preference for Resident Contractors**. For a public works bid received from a nonresident contractor from a state that provides an in-state percentage bidding preference, a Comparable Percentage Disadvantage (CPD) will be applied to the bid of that nonresident contractor. The CPD is the in-state contractor percent advantage provided by the contractor's home state.

   For the purpose of determining the successful bidder, multiply the Nonresident Contractor bid amount by the CPD. The "bid amount" shall be the total of the base bid and all accepted alternate bid items. The CPD shall be added to the Nonresident

Contractor bid amount which equates to the Nonresident Disadvantage Total. The Nonresident Disadvantage Total shall be compared to the Washington contractor bid amounts. The bidder with the lowest total shall be the successful bidder. See example below:

EXAMPLE: Alaska Nonresident Contractor Bid Amount	$100,000
Multiplied by the Alaska CPD	x 0.05
Alaska CPD Total	$ 5,000
Alaska Nonresident Contractor Bid Amount	$100,000
Alaska CPD Total	$ 5,000
Nonresident Disadvantage Total	$105,000*

* Note – If the Nonresident Disadvantage Total is lower than all other Washington contractor bid amounts, the Alaska Nonresident Contractor is the successful bidder and will be awarded a contract for the bid amount of $100,000.

If the Nonresident Disadvantage Total is higher than a Washington contractor bid amount, the successful Washington bidder will be awarded a contract for the bid amount.

F. The Contract will only become effective when signed by the Owner. Prior to the Owner's signature, any and all costs incurred shall be the sole responsibility of the bidder.

1.13 DOCUMENTS (ATTACHED)

A. Advertisement for Bids
B. Responsibility Criteria (if applicable)
C. Bid Proposal
D. Washington State Prevailing Wage Rates
E. Certificate of Insurance form

Note: AIA Payment Bond and Performance Bond forms (A312) are required. These forms will not be provided by the Owner.

Section	Description	Page
PART 1 – GENERAL PROVISIONS		
1.01	Definitions	3
1.02	Order of Precedence	4
1.03	Execution and Intent	5
PART 2 – INSURANCE AND BONDS		
2.01	Contractor's Liability Insurance	5
2.02	Coverage Limits	6
2.03	Insurance Coverage Certificates	6
2.04	Payment and Performance Bonds	6
2.05	Alternative Surety	7
2.06	Builder's Risk	7
PART 3 – TIME AND SCHEDULE		
3.01	Progress and Completion	7
3.02	Construction Schedule	7
3.03	Owner's Right to Suspend the Work for Convenience	8
3.04	Owner's Right to Stop the Work for Cause	9
3.05	Delay	9
3.06	Notice to Owner of Labor Disputes	10
3.07	Damages for Failure to Achieve Timely Completion	10
PART 4 – SPECIFICATIONS, DRAWINGS, AND OTHER DOCUMENTS		
4.01	Discrepancies and Contract Document Review	11
4.02	Project Record	11
4.03	Shop Drawings	12
4.04	Organization of Specifications	13
4.05	Ownership and Use of Drawings, Specifications & other Documents	13
PART 5 – PERFORMANCE		
5.01	Contractor Control and Supervision	13
5.02	Permits, Fees and Notices	14
5.03	Patents and Royalties	14
5.04	Prevailing Wages	15
5.05	Hours of Labor	15
5.06	Nondiscrimination	16
5.07	Safety Precautions	16
5.08	Operations, Material Handling, and Storage Areas	18
5.09	Prior Notice of Excavation	19
5.10	Unforeseen Physical Conditions	19
5.11	Protection of Existing Structures, Equipment, Vegetation, Utilities, & Improvements	19
5.12	Layout of Work	19
5.13	Material and Equipment	20
5.14	Availability and Use of Utility Services	20
5.15	Tests and Inspections	20
5.16	Correction of Nonconforming Work	21
5.17	Clean Up	22
5.18	Access to Work	22
5.19	Other Contracts	23
5.20	Subcontractors and Suppliers	23
5.21	Warranty of Construction	24

PART 5 – PERFORMANCE (continued)

5.22 Indemnification…… 25

PART 6 – PAYMENTS AND COMPLETION

6.01 Contract 25
6.02 Schedule of Values…… 25
6.03 Application for Payment…… 25
6.04 Progress Payments…… 26
6.05 Payments Withheld…… 27
6.06 Retainage and Bond Claim Rights…… 27
6.07 Substantial Completion…… 27
6.08 Prior Occupancy…… 28
6.09 Final Completion, Acceptance, and Payment…… 28

PART 7 – CHANGES

7.01 Change in the Work…… 28
7.02 Change in the Contract Sum…… 30
7.03 Change in the Contract Time…… 36

PART 8 – CLAIMS AND DISPUTE RESOLUTION

8.01 Claims Procedure…… 38
8.02 Arbitration…… 39
8.03 Claims Audits…… 40

PART 9 – TERMINATION OF THE WORK

9.01 Termination by Owner for Cause…… 41
9.02 Termination by Owner for Convenience…… 42

PART 10 – MISCELLANEOUS PROVISIONS

10.01 Governing Law…… 43
10.02 Successors and Assigns…… 43
10.03 Meaning of Words…… 43
10.04 Rights and Remedies…… 44
10.05 Contractor Registration…… 44
10.06 Time Computations…… 44
10.07 Records Retention…… 44
10.08 Third-Party Agreements…… 44
10.09 Antitrust Assignments…… 44
10.10 Headings and Captions…… 44

PART 1 – GENERAL PROVISIONS

1.1 DEFINITIONS

A. "Application for Payment" means a written request submitted by Contractor to A/E for payment of Work completed in accordance with the Contract Documents and approved Schedule of Values, supported by such substantiating data as Owner or A/E may require.

B. "Architect," "Engineer," or "A/E" means a person or entity lawfully entitled to practice architecture or engineering, representing Owner within the limits of its delegated authority.

C. "Change Order" means a written instrument signed by Owner and Contractor stating their agreement upon all of the following: (1) a change in the Work; (2) the amount of the adjustment in the Contract Sum, if any, and (3) the extent of the adjustment in the Contract Time, if any.

D. "Claim" means Contractor's exclusive remedy for resolving disputes with Owner regarding the terms of a Change Order or a request for equitable adjustment, as more fully set forth in Part 8.

E. "Contract Award Amount" is the sum of the Base Bid and any accepted Alternates.

F. "Contract Documents" means the Advertisement for Bids, Instructions for Bidders, completed Bid Form, General Conditions, Modifications to the General Conditions, Supplemental Conditions, Public Works Contract, other Special Forms, Drawings and Specifications, and all addenda and modifications thereof.

G. "Contract Sum" is the total amount payable by Owner to Contractor, for performance of the Work in accordance with the Contract Documents, including all taxes imposed by law and properly chargeable to the Work, except Washington State sales tax.

H. "Contract Time" is the number of calendar days allotted in the Contract Documents for achieving Substantial Completion of the Work.

I. "Contractor" means the person or entity who has agreed with Owner to perform the Work in accordance with the Contract Documents.

J. "Day(s)" Unless otherwise specified, day(s) shall mean calendar day(s)."

K. "Drawings" are the graphic and pictorial portions of the Contract Documents showing the design, location, and dimensions of the Work, and may include plans, elevations, sections, details, schedules, and diagrams.

L. "Final Acceptance" means the written acceptance issued to Contractor by Owner after Contractor has completed the requirements of the Contract Documents, as more fully set forth in Section 6.09 B.

M. "Final Completion" means that the Work is fully and finally complete in accordance with the Contract Documents, as more fully set forth in Section 6.09 A.

N. "Force Majeure" means those acts entitling Contractor to request an equitable adjustment in the Contract Time, as more fully set forth in paragraph 3.05A.

O. "Notice" means a written notice which has been delivered in person to the individual or a member of the firm or entity or to an officer of the corporation for which it was intended or, if delivered or sent by registered or certified mail, to the last business address known to the party giving notice.

P. "Notice to Proceed" means a notice from Owner to Contractor that defines the date on which the Contract Time begins to run.

Q. "Owner" means the state agency, institution, or its authorized representative with the authority to enter into, administer, and/or terminate the Work in accordance with the Contract Documents and make related determinations and findings.

R. "Person" means a corporation, partnership, business association of any kind, trust, company, or individual.

S. "Prior Occupancy" means Owner's use of all or parts of the Project before Substantial Completion, as more fully set forth in Section 6.08 A.

T. "Progress Schedule" means a schedule of the Work, in a form satisfactory to Owner, as further set forth in Section 3.02.

U. "Project" means the total construction of which the Work performed in accordance with the Contract Documents may be the whole or a part and which may include construction by Owner or by separate contractors.

V. "Project Record" means the separate set of Drawings and Specifications as further set forth in paragraph 4.02A.

W. "Sched le of Values" means a written breakdown allocating the total Contract Sum to each principal category of Work, in such detail as requested by Owner.

X. "Specifications" are that portion of the Contract Documents consisting of the written requirements for materials, equipment, construction systems, standards and workmanship for the Work, and performance of related services.

Y. "Subcontract" means a contract entered into by Subcontractor for the purpose of obtaining supplies, materials, equipment, or services of any kind for or in connection with the Work.

Z. "Subcontractor" means any person, other than Contractor, who agrees to furnish or furnishes any supplies, materials, equipment, or services of any kind in connection with the Work.

AA. "Substantial Completion" means that stage in the progress of the Work when the construction is sufficiently complete, as more fully set forth in Section 6.07.

AB. "Work" means the construction and services required by the Contract Documents, and includes, but is not limited to, labor, materials, supplies, equipment, services, permits, and the manufacture and fabrication of components, performed, furnished, or provided in accordance with the Contract Documents.

1.2 ORDER OF PRECEDENCE

Any conflict or inconsistency in the Contract Documents shall be resolved by giving the documents precedence in the following order:

1. Signed Public Works Contract, including any Change Orders.

2. Supplemental Conditions.

3. Modifications to the General Conditions.

4. General Conditions.

5. Specifications. Provisions in Division 1 shall take precedence over provisions of any other Division.

6. Drawings. In case of conflict within the Drawings, large scale drawings shall take precedence over small scale drawings.

7. Signed and Completed Bid Form.

8. Instructions to Bidders.

9. Advertisement for Bids.

1.3 EXECUTION AND INTENT

Contractor Representations: Contractor makes the following representations to Owner:

1. Contract Sum reasonable: The Contract Sum is reasonable compensation for the Work and the Contract Time is adequate for the performance of the Work, as represented by the Contract Documents;

2. Contractor familiar with project: Contractor has carefully reviewed the Contract Documents, visited and examined the Project site, become familiar with the local conditions in which the Work is to be performed, and satisfied itself as to the nature, location, character, quality and quantity of the Work, the labor, materials, equipment, goods, supplies, work, services and other items to be furnished and all other requirements of the Contract Documents, as well as the surface and subsurface conditions and other matters that may be encountered at the Project site or affect performance of the Work or the cost or difficulty thereof;

3. Contractor financially capable: Contractor is financially solvent, able to pay its debts as they mature, and possesses sufficient working capital to complete the Work and perform Contractor's obligations required by the Contract Documents; and

4. Contractor can complete Work: Contractor is able to furnish the plant, tools, materials, supplies, equipment and labor required to complete the Work and perform the obligations required by the Contract Documents and has sufficient experience and competence to do so.

PART 2 – INSURANCE AND BONDS

2.1 CONTRACTOR'S LIABILITY INSURANCE

General insurance requirements: Prior to commencement of the Work, Contractor shall obtain all the insurance required by the Contract Documents and provide evidence satisfactory to Owner that such insurance has been procured. Review of the Contractor's insurance by Owner shall not relieve or decrease the liability of Contractor. Companies writing the insurance to be obtained by this part shall be licensed to do business under Chapter 48 RCW or comply with the Surplus Lines Law of the State of Washington. Contractor shall include in its bid the cost of all insurance and bond costs required to complete the base bid work and accepted alternates. Insurance carriers providing insurance in accordance with the Contract Documents shall be acceptable to Owner, and its A.M. Best rating shall be indicated on the insurance certificates.

A. Term of insurance coverage: Contractor shall maintain the following insurance coverage during the Work and for one year after Final Acceptance. Contractor shall also maintain the following insurance coverage during the performance of any corrective Work required by Section 5.16.

1. General Liability Insurance: Commercial General Liability (CGL) on an Occurrence Form. Coverage shall include, but not be limited to:

   a. Completed operations/products liability;

   b. Explosion, collapse, and underground; and

   c. Employer's liability coverage.

2. Automobile Liability Insurance: Automobile liability

B. Industrial Insurance compliance: Contractor shall comply with the Washington State Industrial Insurance Act and, if applicable, the Federal Longshoremen's and Harbor Workers' Act and the Jones Act.

C. Insurance to protect for the following: All insurance coverages shall protect against claims for damages for personal and bodily injury or death, as well as claims for property damage, which may arise from operations in connection with the Work whether such operations are by Contractor or any Subcontractor.

D. Owner as Additional Insured: All insurance coverages shall be endorsed to include Owner as an additional named insured for Work performed in accordance with the Contract Documents, and all insurance certificates shall evidence the Owner as an additional insured.

2.2 COVERAGE LIMITS

Insurance amounts: The coverage limits shall be as follows:

A. Limits of Liability shall not be less than $1,000,000 Combined Single Limit for Bodily Injury and Property Damage (other than Automobile Liability) Each Occurrence; Personal Injury and Advertising Liability Each Occurrence.

B. $2,000,000 Combined Single Limit Annual General Aggregate.

C. $2,000,000 Annual Aggregate for Products and Completed Operations Liability.

D. $1,000,000 Combined Single Limit for Automobile Bodily Injury and Property Damage Liability, Each Accident or Loss.

2.3 INSURANCE COVERAGE CERTIFICATES

A. Certificate required: Prior to commencement of the Work, Contractor shall furnish to Owner a completed certificate of insurance coverage.

B. List Project info: All insurance certificates shall name Owner's Project number and Project title.

C. Cancellation provisions: All insurance certificates shall specifically require 45 Days prior notice to Owner of cancellation or any material change, except 30 Days for surplus line insurance.

2.4 PAYMENT AND PERFORMANCE BONDS

Conditions for bonds: Payment and performance bonds for 100% of the Contract Award Amount, plus state sales tax, shall be furnished for the Work, using the Payment Bond and Performance Bond form published by and available from the American Institute of Architects (AIA) – form A312. Prior to execution of a Change Order that, cumulatively with previous Change Orders, increases the Contract Award Amount by 15% or more, the Contractor shall provide either new payment and performance bonds for the

revised Contract Sum, or riders to the existing payment and performance bonds increasing the amount of the bonds. The Contractor shall likewise provide additional bonds or riders when subsequent Change Orders increase the Contract Sum by 15% or more. No payment or performance bond is required if the Contract Sum is $35,000 or less and Contractor agrees that Owner may, in lieu of the bond, retain 50% of the Contract Sum for the period allowed by RCW 39.08.010.

2.5 ALTERNATIVE SURETY

When alternative surety required: Contractor shall promptly furnish payment and performance bonds from an alternative surety as required to protect Owner and persons supplying labor or materials required by the Contract Documents if:

A. Owner has a reasonable objection to the surety; or

B. Any surety fails to furnish reports on its financial condition if required by Owner.

2.6 BUILDER'S RISK

A. Contractor to buy Property Insurance: Contractor shall purchase and maintain property insurance in the amount of the Contract Sum including all Change Orders for the Work on a replacement cost basis until Substantial Completion. For projects not involving New Building Construction, "Installation Floater" is an acceptable substitute for the Builder's Risk Insurance. The insurance shall cover the interest of Owner, Contractor, and any Subcontractors, as their interests may appear.

B. Losses covered: Contractor property insurance shall be placed on an "all risk" basis and insure against the perils of fire and extended coverage and physical loss or damage including theft, vandalism, malicious mischief, collapse, false work, temporary buildings, debris removal including demolition occasioned by enforcement of any applicable legal requirements, and shall cover reasonable compensation for A/E's services and expenses required as a result of an insured loss.

C. Waiver of subrogation rights: Owner and Contractor waive all subrogation rights against each other, any Subcontractors, A/E, A/E's sub-consultants, separate contractors described in Section 5.20, if any, and any of their subcontractors, for damages caused by fire or other perils to the extent covered by property insurance obtained pursuant to this section or other property insurance applicable to the Work, except such rights as they have to proceeds of such insurance held by Owner as fiduciary. The policies shall provide such waivers of subrogation by endorsement or otherwise. A waiver of subrogation shall be effective to a person or entity even though that person or entity would otherwise have a duty of indemnification, contractual or otherwise, did not pay the insurance premium directly or indirectly, and whether or not the person or entity had an insurable interest in the property damaged.

PART 3 – TIME AND SCHEDULE

3.1 PROGRESS AND COMPLETION

Contractor to meet schedule: Contractor shall diligently prosecute the Work, with adequate forces, achieve Substantial Completion within the Contract Time, and achieve Final Completion within a reasonable period thereafter.

3.2 CONSTRUCTION SCHEDULE

A. Preliminary Progress Schedule: Unless otherwise provided in Division 1, Contractor shall, within 14 Days after issuance of the Notice to Proceed, submit a preliminary Progress Schedule. The Progress Schedule shall show the sequence in which Contractor proposes to perform the Work,

and the dates on which Contractor plans to start and finish major portions of the Work, including dates for shop drawings and other submittals, and for acquiring materials and equipment.

B. Form of Progress Schedule: Unless otherwise provided in Division 1, the Progress Schedule shall be in the form of a bar chart, or a critical path method analysis, as specified by Owner. The preliminary Progress Schedule may be general, showing the major portions of the Work, with a more detailed Progress Schedule submitted as directed by Owner.

C. Owner comments on Progress Schedule: Owner shall return comments on the preliminary Progress Schedule to Contractor within 14 Days of receipt. Review by Owner of Contractor's schedule does not constitute an approval or acceptance of Contractor's construction means, methods, or sequencing, or its ability to complete the Work within the Contract Time. Contractor shall revise and resubmit its schedule, as necessary. Owner may withhold a portion of progress payments until a Progress Schedule has been submitted which meets the requirements of this section.

D. Monthly updates and compliance with Progress Schedule: Contractor shall utilize and comply with the Progress Schedule. On a monthly basis, or as otherwise directed by Owner, Contractor shall submit an updated Progress Schedule at its own expense to Owner indicating actual progress. If, in the opinion of Owner, Contractor is not in conformance with the Progress Schedule for reasons other than acts of Force Majeure as identified in Section 3.05, Contractor shall take such steps as are necessary to bring the actual completion dates of its work activities into conformance with the Progress Schedule, and if directed by Owner, Contractor shall submit a corrective action plan or revise the Progress Schedule to reconcile with the actual progress of the Work.

E. Contractor to notify Owner of delays: Contractor shall promptly notify Owner in writing of any actual or anticipated event which is delaying or could delay achievement of any milestone or performance of any critical path activity of the Work. Contractor shall indicate the expected duration of the delay, the anticipated effect of the delay on the Progress Schedule, and the action being or to be taken to correct the problem. Provision of such notice does not relieve Contractor of its obligation to complete the Work within the Contract Time.

3.3 OWNER'S RIGHT TO SUSPEND THE WORK FOR CONVENIENCE

A. Owner may suspend Work: Owner may, at its sole discretion, order Contractor, in writing, to suspend all or any part of the Work for up to 90 Days, or for such longer period as mutually agreed.

B. Compliance with suspension; Owner's options: Upon receipt of a written notice suspending the Work, Contractor shall immediately comply with its terms and take all reasonable steps to minimize the incurrence of cost of performance directly attributable to such suspension. Within a period up to 90 Days after the notice is delivered to Contractor, or within any extension of that period to which the parties shall have agreed, Owner shall either:

1. Cancel the written notice suspending the Work; or

2. Terminate the Work covered by the notice as provided in the termination provisions of Part 9.

C. Resumption of Work: If a written notice suspending the Work is cancelled or the period of the notice or any extension thereof expires, Contractor shall resume Work.

D. Equitable Adjustment for suspensions: Contractor shall be entitled to an equitable adjustment in the Contract Time, or Contract Sum, or both, for increases in the time or cost of performance

directly attributable to such suspension, provided Contractor complies with all requirements set forth in Part 7.

3.4 OWNER'S RIGHT TO STOP THE WORK FOR CAUSE

A. Owner may stop Work for Contractor's failure to perform: If Contractor fails or refuses to perform its obligations in accordance with the Contract Documents, Owner may order Contractor, in writing, to stop the Work, or any portion thereof, until satisfactory corrective action has been taken.

B. No Equitable Adjustment for Contractor's failure to perform: Contractor shall not be entitled to an equitable adjustment in the Contract Time or Contract Sum for any increased cost or time of performance attributable to Contractor's failure or refusal to perform or from any reasonable remedial action taken by Owner based upon such failure.

3.5 DELAY

A. Force Majeure actions not a default; Force Majeure defined: Any delay in or failure of performance by Owner or Contractor, other than the payment of money, shall not constitute a default hereunder if and to the extent the cause for such delay or failure of performance was unforeseeable and beyond the control of the party ("Force Majeure"). Acts of Force Majeure include, but are not limited to:

1. Acts of God or the public enemy;

2. Acts or omissions of any government entity;

3. Fire or other casualty for which Contractor is not responsible;

4. Quarantine or epidemic;

5. Strike or defensive lockout;

6. Unusually severe weather conditions which could not have been reasonably anticipated; and

7. Unusual delay in receipt of supplies or products which were ordered and expedited and for which no substitute reasonably acceptable to Owner was available.

B. Contract Time adjustment for Force Majeure: Contractor shall be entitled to an equitable adjustment in the Contract Time for changes in the time of performance directly attributable to an act of Force Majeure, provided it makes a request for equitable adjustment according to Section 7.03. Contractor shall not be entitled to an adjustment in the Contract Sum resulting from an act of Force Majeure.

C. Contract Time or Contract Sum adjustment if Owner at fault: Contractor shall be entitled to an equitable adjustment in Contract Time, and may be entitled to an equitable adjustment in Contract Sum, if the cost or time of Contractor's performance is changed due to the fault or negligence of Owner, provided the Contractor makes a request according to Sections 7.02 and 7.03.

D. No Contract Time or Contract Sum adjustment if Contractor at fault: Contractor shall not be entitled to an adjustment in Contract Time or in the Contract Sum for any delay or failure of performance to the extent such delay or failure was caused by Contractor or anyone for whose acts Contractor is responsible.

E. Contract Time adjustment only for concurrent fault: To the extent any delay or failure of performance was concurrently caused by the Owner and Contractor, Contractor shall be entitled to an adjustment in the Contract Time for that portion of the delay or failure of performance that was concurrently caused, provided it makes a request for equitable adjustment according to Section 7.03, but shall not be entitled to an adjustment in Contract Sum.

F. Contractor to mitigate delay impacts: Contractor shall make all reasonable efforts to prevent and mitigate the effects of any delay, whether occasioned by an act of Force Majeure or otherwise.

3.6 NOTICE TO OWNER OF LABOR DISPUTES

A. Contractor to notify Owner of labor disputes: If Contractor has knowledge that any actual or potential labor dispute is delaying or threatens to delay timely performance in accordance with the Contract Documents, Contractor shall immediately give notice, including all relevant information, to Owner.

B. Pass through notification provisions to Subcontractors: Contractor agrees to insert a provision in its Subcontracts and to require insertion in all sub-subcontracts, that in the event timely performance of any such contract is delayed or threatened by delay by any actual or potential labor dispute, the Subcontractor or Sub-subcontractor shall immediately notify the next higher tier Subcontractor or Contractor, as the case may be, of all relevant information concerning the dispute.

3.7 DAMAGES FOR FAILURE TO ACHIEVE TIMELY COMPLETION

A. Liquidated Damages

1. Reason for Liquidated Damages: Timely performance and completion of the Work is essential to Owner and time limits stated in the Contract Documents are of the essence. Owner will incur serious and substantial damages if Substantial Completion of the Work does not occur within the Contract Time. However, it would be difficult if not impossible to determine the exact amount of such damages. Consequently, provisions for liquidated damages are included in the Contract Documents.

2. Calculation of Liquidated Damages amount: The liquidated damage amounts set forth in the Contract Documents will be assessed not as a penalty, but as liquidated damages for breach of the Contract Documents. This amount is fixed and agreed upon by and between the Contractor and Owner because of the impracticability and extreme difficulty of fixing and ascertaining the actual damages the Owner would in such event sustain. This amount shall be construed as the actual amount of damages sustained by the Owner, and may be retained by the Owner and deducted from periodic payments to the Contractor.

3. Contractor responsible even if Liquidated Damages assessed: Assessment of liquidated damages shall not release Contractor from any further obligations or liabilities pursuant to the Contract Documents.

B. Actual Damages

Calculation of Actual Damages: Actual damages will be assessed for failure to achieve Final Completion within the time provided. Actual damages will be calculated on the basis of direct architectural, administrative, and other related costs attributable to the Project from the date when Final Completion should have been achieved, based on the date Substantial Completion is actually achieved, to the date Final Completion is actually achieved. Owner may offset these costs against any payment due Contractor.

PART 4 – SPECIFICATIONS, DRAWINGS, AND OTHER DOCUMENTS

4.1 DISCREPANCIES AND CONTRACT DOCUMENT REVIEW

A. Specifications and Drawings are basis of the Work: The intent of the Specifications and Drawings is to describe a complete Project to be constructed in accordance with the Contract Documents. Contractor shall furnish all labor, materials, equipment, tools, transportation, permits, and supplies, and perform the Work required in accordance with the Drawings, Specifications, and other provisions of the Contract Documents.

B. Parts of the Contract Documents are complementary: The Contract Documents are complementary. What is required by one part of the Contract Documents shall be binding as if required by all. Anything mentioned in the Specifications and not shown on the Drawings, or shown on the Drawings and not mentioned in the Specifications, shall be of like effect as if shown or mentioned in both.

C. Contractor to report discrepancies in Contract Documents: Contractor shall carefully study and compare the Contract Documents with each other and with information furnished by Owner. If, during the performance of the Work, Contractor finds a conflict, error, inconsistency, or omission in the Contract Documents, it shall promptly and before proceeding with the Work affected thereby, report such conflict, error, inconsistency, or omission to A/E in writing.

D. Contractor knowledge of discrepancy in documents – responsibility: Contractor shall do no Work without applicable Drawings, Specifications, or written modifications, or Shop Drawings where required, unless instructed to do so in writing by Owner. If Contractor performs any construction activity, and it knows or reasonably should have known that any of the Contract Documents contain a conflict, error, inconsistency, or omission, Contractor shall be responsible for the performance and shall bear the cost for its correction.

E. Contractor to perform Work implied by Contract Documents: Contractor shall provide any work or materials the provision of which is clearly implied and is within the scope of the Contract Documents even if the Contract Documents do not mention them specifically.

F. Interpretation questions referred to A/E: Questions regarding interpretation of the requirements of the Contract Documents shall be referred to the A/E.

4.2 PROJECT RECORD

A. Contractor to maintain Project Record Drawings and Specifications: Contractor shall legibly mark in ink on a separate set of the Drawings and Specifications all actual construction, including depths of foundations, horizontal and vertical locations of internal and underground utilities and appurtenances referenced to permanent visible and accessible surface improvements, field changes of dimensions and details, actual suppliers, manufacturers and trade names, models of installed equipment, and Change Order Proposals (COP). This separate set of Drawings and Specifications shall be the “Project Record.”

B. Update Project Record weekly and keep on site: The Project Record shall be maintained on the project site throughout the construction and shall be clearly labeled “PROJECT RECORD.” The Project Record shall be updated at least weekly noting all changes and shall be available to Owner at all times.

C. Final Project Record to A/E before Final Acceptance: Contractor shall submit the completed and finalized Project Record to A/E prior to Final Acceptance.

4.3 SHOP DRAWINGS

A. Definition of Shop Drawings: "Shop Drawings" means documents and other information required to be submitted to A/E by Contractor pursuant to the Contract Documents, showing in detail: the proposed fabrication and assembly of structural elements; and the installation (i.e. form, fit, and attachment details) of materials and equipment. Shop Drawings include, but are not limited to, drawings, diagrams, layouts, schematics, descriptive literature, illustrations, schedules, performance and test data, samples, and similar materials furnished by Contractor to explain in detail specific portions of the Work required by the Contract Documents. For materials and equipment to be incorporated into the Work, Contractor submittal shall include the name of the manufacturer, the model number, and other information concerning the performance, capacity, nature, and rating of the item. When directed, Contractor shall submit all samples at its own expense. Owner may duplicate, use, and disclose Shop Drawings provided in accordance with the Contract Documents.

B. Approval of Shop Drawings by Contractor and A/E: Contractor shall coordinate all Shop Drawings, and review them for accuracy, completeness, and compliance with the Contract Documents and shall indicate its approval thereon as evidence of such coordination and review. Where required by law, Shop Drawings shall be stamped by an appropriate professional licensed by the state of Washington. Shop Drawings submitted to A/E without evidence of Contractor's approval shall be returned for resubmission. Contractor shall review, approve, and submit Shop Drawings with reasonable promptness and in such sequence as to cause no delay in the Work or in the activities of Owner or separate contractors. Contractor's submittal schedule shall allow a reasonable time for A/E review. A/E will review, approve, or take other appropriate action on the Shop Drawings. Contractor shall perform no portion of the Work requiring submittal and review of Shop Drawings until the respective submittal has been reviewed and the A/E has approved or taken other appropriate action. Owner and A/E shall respond to Shop Drawing submittals with reasonable promptness. Any Work by Contractor shall be in accordance with reviewed Shop Drawings. Submittals made by Contractor which are not required by the Contract Documents may be returned without action.

C. Contractor not relieved of responsibility when Shop Drawings approved: Approval, or other appropriate action with regard to Shop Drawings, by Owner or A/E shall not relieve Contractor of responsibility for any errors or omissions in such Shop Drawings, nor from responsibility for compliance with the requirements of the Contract Documents. Unless specified in the Contract Documents, review by Owner or A/E shall not constitute an approval of the safety precautions employed by Contractor during construction, or constitute an approval of Contractor's means or methods of construction. If Contractor fails to obtain approval before installation and the item or work is subsequently rejected, Contractor shall be responsible for all costs of correction.

D. Variations between Shop Drawings and Contract Documents: If Shop Drawings show variations from the requirements of the Contract Documents, Contractor shall describe such variations in writing, separate from the Shop Drawings, at the time it submits the Shop Drawings containing such variations. If A/E approves any such variation, an appropriate Change Order will be issued. If the variation is minor and does not involve an adjustment in the Contract Sum or Contract Time, a Change Order need not be issued; however, the modification shall be recorded upon the Project Record.

E. Contractor to submit 5 copies of Shop Drawings: Unless otherwise provided in Division 1, Contractor shall submit to A/E for approval 5 copies of all Shop Drawings. Unless otherwise indicated, 3 sets of all Shop Drawings shall be retained by A/E and 2 sets shall be returned to Contractor.

4.4 ORGANIZATION OF SPECIFICATIONS

Specification organization by trade: Specifications are prepared in sections which conform generally with trade practices. These sections are for Owner and Contractor convenience and shall not control Contractor in dividing the Work among the Subcontractors or in establishing the extent of the Work to be performed by any trade.

4.5 OWNERSHIP AND USE OF DRAWINGS, SPECIFICATIONS, AND OTHER DOCUMENTS

A. A/E, not Contractor, owns Copyright of Drawings and Specifications: The Drawings, Specifications, and other documents prepared by A/E are instruments of A/E's service through which the Work to be executed by Contractor is described. Neither Contractor nor any Subcontractor shall own or claim a copyright in the Drawings, Specifications, and other documents prepared by A/E, and A/E shall be deemed the author of them and will, along with any rights of Owner, retain all common law, statutory, and other reserved rights, in addition to the copyright. All copies of these documents, except Contractor's set, shall be returned or suitably accounted for to A/E, on request, upon completion of the Work.

B. Drawings and Specifications to be used only for this Project: The Drawings, Specifications, and other documents prepared by the A/E, and copies thereof furnished to Contractor, are for use solely with respect to this Project. They are not to be used by Contractor or any Subcontractor on other projects or for additions to this Project outside the scope of the Work without the specific written consent of Owner and A/E. Contractor and Subcontractors are granted a limited license to use and reproduce applicable portions of the Drawings, Specifications, and other documents prepared by A/E appropriate to and for use in the execution of their Work.

C. Shop Drawing license granted to Owner: Contractor and all Subcontractors grant a non-exclusive license to Owner, without additional cost or royalty, to use for its own purposes (including reproduction) all Shop Drawings, together with the information and diagrams contained therein, prepared by Contractor or any Subcontractor. In providing Shop Drawings, Contractor and all Subcontractors warrant that they have authority to grant to Owner a license to use the Shop Drawings, and that such license is not in violation of any copyright or other intellectual property right. Contractor agrees to defend and indemnify Owner pursuant to the indemnity provisions in Section 5.03 and 5.22 from any violations of copyright or other intellectual property rights arising out of Owner's use of the Shop Drawings hereunder, or to secure for Owner, at Contractor's own cost, licenses in conformity with this section.

D. Shop Drawings to be used only for this Project: The Shop Drawings and other submittals prepared by Contractor, Subcontractors of any tier, or its or their equipment or material suppliers, and copies thereof furnished to Contractor, are for use solely with respect to this Project. They are not to be used by Contractor or any Subcontractor of any tier, or material or equipment supplier, on other projects or for additions to this Project outside the scope of the Work without the specific written consent of Owner. The Contractor, Subcontractors of any tier, and material or equipment suppliers are granted a limited license to use and reproduce applicable portions of the Shop Drawings and other submittals appropriate to and for use in the execution of their Work under the Contract Documents.

PART 5 – PERFORMANCE

5.1 CONTRACTOR CONTROL AND SUPERVISION

A. Contractor responsible for Means and Methods of construction: Contractor shall supervise and direct the Work, using its best skill and attention, and shall perform the Work in a skillful manner. Contractor shall be solely responsible for and have control over construction means, methods, techniques, sequences, and procedures and for coordinating all portions of the Work, unless the

Contract Documents give other specific instructions concerning these matters. Contractor shall disclose its means and methods of construction when requested by Owner.

B. Competent Superintendent required: Performance of the Work shall be directly supervised by a competent superintendent who has authority to act for Contractor. The superintendent must be satisfactory to the Owner and shall not be changed without the prior written consent of Owner. Owner may require Contractor to remove the superintendent from the Work or Project site, if Owner reasonably deems the superintendent incompetent, careless, or otherwise objectionable, provided Owner has first notified Contractor in writing and allowed a reasonable period for transition.

C. Contractor responsible for acts and omissions of self and agents: Contractor shall be responsible to Owner for acts and omissions of Contractor, Subcontractors, and their employees and agents.

D. Contractor to employ competent and disciplined workforce: Contractor shall enforce strict discipline and good order among all of the Contractor's employees and other persons performing the Work. Contractor shall not permit employment of persons not skilled in tasks assigned to them. Contractor's employees shall at all times conduct business in a manner which assures fair, equal, and nondiscriminatory treatment of all persons. Owner may, by written notice, request Contractor to remove from the Work or Project site any employee Owner reasonably deems incompetent, careless, or otherwise objectionable.

E. Contractor to keep project documents on site: Contractor shall keep on the Project site a copy of the Drawings, Specifications, addenda, reviewed Shop Drawings, and permits and permit drawings.

F. Contractor to comply with ethical standards: Contractor shall ensure that its owner(s) and employees, and those of its Subcontractors, comply with the Ethics in Public Service Act RCW 42.52, which, among other things, prohibits state employees from having an economic interest in any public works contract that was made by, or supervised by, that employee. Contractor shall remove, at its sole cost and expense, any of its, or its Subcontractors' employees, if they are in violation of this act.

5.2 PERMITS, FEES, AND NOTICES

A. Contractor to obtain and pay for permits: Unless otherwise provided in the Contract Documents, Contractor shall pay for and obtain all permits, licenses, and inspections necessary for proper execution and completion of the Work. Prior to Final Acceptance, the approved, signed permits shall be delivered to Owner.

B. Allowances for permit fees: If allowances for permits or utility fees are called for in the Contract Documents and set forth in Contractor's bid, and the actual costs of those permits or fees differ from the allowances in the Contract Documents, the difference shall be adjusted by Change Order.

C. Contractor to comply with all applicable laws: Contractor shall comply with and give notices required by all federal, state, and local laws, ordinances, rules, regulations, and lawful orders of public authorities applicable to performance of the Work.

5.3 PATENTS AND ROYALTIES

Payment, indemnification, and notice: Contractor is responsible for, and shall pay, all royalties and license fees. Contractor shall defend, indemnify, and hold Owner harmless from any costs, expenses, and liabilities arising out of the infringement by Contractor of any patent, copyright, or other intellectual property right used in the Work; however, provided that Contractor gives prompt notice, Contractor shall not be responsible for such defense or indemnity when a particular design, process, or product of a

particular manufacturer or manufacturers is required by the Contract Documents. If Contractor has reason to believe that use of the required design, process, or product constitutes an infringement of a patent or copyright, it shall promptly notify Owner of such potential infringement.

5.4 PREVAILING WAGES

A. Contractor to pay Prevailing Wages: Contractor shall pay the prevailing rate of wages to all workers, laborers, or mechanics employed in the performance of any part of the Work in accordance with RCW 39.12 and the rules and regulations of the Department of Labor and Industries. The schedule of prevailing wage rates for the locality or localities of the Work, is determined by the Industrial Statistician of the Department of Labor and Industries. It is the Contractor's responsibility to verify the applicable prevailing wage rate.

B. Statement of Intent to Pay Prevailing Wages: Before payment is made by the Owner to the Contractor for any work performed by the Contractor and subcontractors whose work is included in the application for payment, the Contractor shall submit, or shall have previously submitted to the Owner for the Project, a Statement of Intent to Pay Prevailing Wages, approved by the Department of Labor and Industries, certifying the rate of hourly wage paid and to be paid each classification of laborers, workers, or mechanics employed upon the Work by Contractor and Subcontractors. Such rates of hourly wage shall not be less than the prevailing wage rate.

C. Affidavit of Wages Paid: Prior to release of retainage, the Contractor shall submit to the Owner an Affidavit of Wages Paid, approved by the Department of Labor and Industries, for the Contractor and every subcontractor, of any tier, that performed work on the Project.

D. Disputes: Disputes regarding prevailing wage rates shall be referred for arbitration to the Director of the Department of Labor and Industries. The arbitration decision shall be final and conclusive and binding on all parties involved in the dispute as provided for by RCW 39.12.060.

E. Statement with pay application; Post Statements of Intent at job site: Each Application for Payment submitted by Contractor shall state that prevailing wages have been paid in accordance with the pre-filed statement(s) of intent, as approved. Copies of the approved intent statement(s) shall be posted on the job site with the address and telephone number of the Industrial Statistician of the Department of Labor and Industries where a complaint or inquiry concerning prevailing wages may be made.

F. Contractor to pay for Statements of Intent and Affidavits: In compliance with chapter 296-127 WAC, Contractor shall pay to the Department of Labor and Industries the currently established fee(s) for each statement of intent and/or affidavit of wages paid submitted to the Department of Labor and Industries for certification.

G. Certified Payrolls: Consistent with WAC 296-127-320, the Contractor and any subcontractor shall submit a certified copy of payroll records if requested.

5.5 HOURS OF LABOR

A. Overtime: Contractor shall comply with all applicable provisions of RCW 49.28 and they are incorporated herein by reference. Pursuant to that statute, no laborer, worker, or mechanic employed by Contractor, any Subcontractor, or any other person performing or contracting to do the whole or any part of the Work, shall be permitted or required to work more than eight hours in any one calendar day, provided, that in cases of extraordinary emergency, such as danger to life or property, the hours of work may be extended, but in such cases the rate of pay for time employed in excess of eight hours of each calendar day shall be not less than one and one-half times the rate allowed for this same amount of time during eight hours of service.

B. 4-10 Agreements: Notwithstanding the preceding paragraph, RCW 49.28 permits a contractor or subcontractor in any public works contract subject to those provisions, to enter into an agreement with its employees in which the employees work up to ten hours in a calendar day. No such agreement may provide that the employees work ten-hour days for more than four calendar days a week. Any such agreement is subject to approval by the employees. The overtime provisions of RCW 49.28 shall not apply to the hours, up to forty hours per week, worked pursuant to any such agreement.

5.6 NONDISCRIMINATION

A. Discrimination prohibited by applicable laws: Discrimination in all phases of employment is prohibited by, among other laws and regulations, Title VII of the Civil Rights Act of 1964, the Vietnam Era Veterans Readjustment Act of 1974, Sections 503 and 504 of the Vocational Rehabilitation Act of 1973, the Equal Employment Act of 1972, the Age Discrimination Act of 1967, the Americans with Disabilities Act of 1990, the Civil Rights Act of 1991, Presidential Executive Order 11246, Executive Order 11375, the Washington State Law Against Discrimination, RCW 49.60, and Gubernatorial Executive Order 85-09. These laws and regulations establish minimum requirements for affirmative action and fair employment practices which Contractor must meet.

B. During performance of the Work:

1. Protected Classes: Contractor shall not discriminate against any employee or applicant for employment because of race, creed, color, national origin, sex, age, marital status, or the presence of any physical, sensory, or mental disability, Vietnam era veteran status, or disabled veteran status, nor commit any other unfair practices as defined in RCW 49.60.

2. Advertisements to state nondiscrimination: Contractor shall, in all solicitations or advertisements for employees placed by or for it, state that all qualified applicants will be considered for employment, without regard to race, creed, color, national origin, sex, age, marital status, or the presence of any physical, sensory, or mental disability.

3. Contractor to notify unions and others of nondiscrimination: Contractor shall send to each labor union, employment agency, or representative of workers with which it has a collective bargaining agreement or other contract or understanding, a notice advising the labor union, employment agency, or workers' representative of Contractor's obligations according to the Contract Documents and RCW 49.60.

4. Owner and State access to Contractor records: Contractor shall permit access to its books, records, and accounts, and to its premises by Owner, and by the Washington State Human Rights Commission, for the purpose of investigation to ascertain compliance with this section of the Contract Documents.

5. Pass through provisions to Subcontractors: Contractor shall include the provisions of this section in every Subcontract.

5.7 SAFETY PRECAUTIONS

A. Contractor responsible for safety: Contractor shall be responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the performance of the Work.

B. Contractor safety responsibilities: In carrying out its responsibilities according to the Contract Documents, Contractor shall protect the lives and health of employees performing the Work and other persons who may be affected by the Work; prevent damage to materials, supplies, and equipment whether on site or stored off-site; and prevent damage to other property at the site or adjacent thereto. Contractor shall comply with all applicable laws, ordinances, rules, regulations,

and orders of any public body having jurisdiction for the safety of persons or property or to protect them from damage, injury, or loss; shall erect and maintain all necessary safeguards for such safety and protection; and shall notify owners of adjacent property and utilities when prosecution of the Work may affect them.

C. Contractor to maintain safety records: Contractor shall maintain an accurate record of exposure data on all incidents relating to the Work resulting in death, traumatic injury, occupational disease, or damage to property, materials, supplies, or equipment. Contractor shall immediately report any such incident to Owner. Owner shall, at all times, have a right of access to all records of exposure.

D. Contractor to provide HazMat training: Contractor shall provide all persons working on the Project site with information and training on hazardous chemicals in their work at the time of their initial assignment, and whenever a new hazard is introduced into their work area.

1. Information. At a minimum, Contractor shall inform persons working on the Project site of:

a. WAC: The requirements of chapter 296-62 WAC, General Occupational Health Standards;

b. Presence of hazardous chemicals: Any operations in their work area where hazardous chemicals are present; and

c. Hazard communications program: The location and availability of written hazard communication programs, including the required list(s) of hazardous chemicals and material safety data sheets required by chapter 296-62 WAC.

2. Training. At a minimum, Contractor shall provide training for persons working on the Project site which includes:

a. Detecting hazardous chemicals: Methods and observations that may be used to detect the presence or release of a hazardous chemical in the work area (such as monitoring conducted by the employer, continuous monitoring devices, visual appearance or odor of hazardous chemicals when being released, etc.);

b. Hazards of chemicals: The physical and health hazards of the chemicals in the work area;

c. Protection from hazards: The measures such persons can take to protect themselves from these hazards, including specific procedures Contractor, or its Subcontractors, or others have implemented to protect those on the Project site from exposure to hazardous chemicals, such as appropriate work practices, emergency procedures, and personal protective equipment to be used; and

d. Hazard communications program: The details of the hazard communications program developed by Contractor, or its Subcontractors, including an explanation of the labeling system and the material safety data sheet, and how employees can obtain and use the appropriate hazard information.

E. Hazardous, toxic or harmful substances: Contractor's responsibility for hazardous, toxic, or harmful substances shall include the following duties:

1. Illegal use of dangerous substances: Contractor shall not keep, use, dispose, transport, generate, or sell on or about the Project site, any substances now or hereafter designated as, or which are subject to regulation as, hazardous, toxic, dangerous, or

harmful by any federal, state or local law, regulation, statute or ordinance (hereinafter collectively referred to as "hazardous substances"), in violation of any such law, regulation, statute, or ordinance, but in no case shall any such hazardous substance be stored more than 90 Days on the Project site.

2. Contractor notifications of spills, failures, inspections, and fines: Contractor shall promptly notify Owner of all spills or releases of any hazardous substances which are otherwise required to be reported to any regulatory agency and pay the cost of cleanup. Contractor shall promptly notify Owner of all failures to comply with any federal, state, or local law, regulation, or ordinance; all inspections of the Project site by any regulatory entity concerning the same; all regulatory orders or fines; and all responses or interim cleanup actions taken by or proposed to be taken by any government entity or private party on the Project site.

F. Public safety and traffic: All Work shall be performed with due regard for the safety of the public. Contractor shall perform the Work so as to cause a minimum of interruption of vehicular traffic or inconvenience to pedestrians. All arrangements to care for such traffic shall be Contractor's responsibilities. All expenses involved in the maintenance of traffic by way of detours shall be borne by Contractor.

G. Contractor to act in an emergency: In an emergency affecting the safety of life or the Work or of adjoining property, Contractor is permitted to act, at its discretion, to prevent such threatened loss or injury, and Contractor shall so act if so authorized or instructed.

H. No duty of safety by Owner or A/E: Nothing provided in this section shall be construed as imposing any duty upon Owner or A/E with regard to, or as constituting any express or implied assumption of control or responsibility over, Project site safety, or over any other safety conditions relating to employees or agents of Contractor or any of its Subcontractors, or the public.

5.8 OPERATIONS, MATERIAL HANDLING, AND STORAGE AREAS

A. Limited storage areas: Contractor shall confine all operations, including storage of materials, to Owner-approved areas.

B. Temporary buildings and utilities at Contractor expense: Temporary buildings (e.g., storage sheds, shops, offices) and utilities may be provided by Contractor only with the consent of Owner and without expense to Owner. The temporary buildings and utilities shall be removed by Contractor at its expense upon completion of the Work.

C. Roads and vehicle loads: Contractor shall use only established roadways or temporary roadways authorized by Owner. When materials are transported in prosecuting the Work, vehicles shall not be loaded beyond the loading capacity recommended by the manufacturer of the vehicle or prescribed by federal, state, or local law or regulation.

D. Ownership and reporting by Contractor of demolished materials: Ownership and control of all materials or facility components to be demolished or removed from the Project site by Contractor shall immediately vest in Contractor upon severance of the component from the facility or severance of the material from the Project site. Contractor shall be responsible for compliance with all laws governing the storage and ultimate disposal. Contractor shall provide Owner with a copy of all manifests and receipts evidencing proper disposal when required by Owner or applicable law.

E. Contractor responsible for care of materials and equipment on-site: Contractor shall be responsible for the proper care and protection of its materials and equipment delivered to the Project site. Materials and equipment may be stored on the premises subject to approval of

Owner. When Contractor uses any portion of the Project site as a shop, Contractor shall be responsible for any repairs, patching, or cleaning arising from such use.

F. Contractor responsible for loss of materials and equipment: Contractor shall protect and be responsible for any damage or loss to the Work, or to the materials or equipment until the date of Substantial Completion, and shall repair or replace without cost to Owner any damage or loss that may occur, except damages or loss caused by the acts or omissions of Owner. Contractor shall also protect and be responsible for any damage or loss to the Work, or to the materials or equipment, after the date of Substantial Completion, and shall repair or replace without cost to Owner any such damage or loss that might occur, to the extent such damages or loss are caused by the acts or omissions of Contractor, or any Subcontractor.

5.9 PRIOR NOTICE OF EXCAVATION

A. Excavation defined; Use of locator services: "Excavation" means an operation in which earth, rock, or other material on or below the ground is moved or otherwise displaced by any means, except the tilling of soil less than 12 inches in depth for agricultural purposes, or road ditch maintenance that does not change the original road grade or ditch flow line. Before commencing any excavation, Contractor shall provide notice of the scheduled commencement of excavation to all owners of underground facilities or utilities, through locator services.

5.10 UNFORESEEN PHYSICAL CONDITIONS

A. Notice requirement for concealed or unknown conditions: If Contractor encounters conditions at the site which are subsurface or otherwise concealed physical conditions which differ materially from those indicated in the Contract Documents, or unknown physical conditions of an unusual nature which differ materially from those ordinarily found to exist and generally recognized as inherent in construction activities of the character provided for in the Contract Documents, then Contractor shall give written notice to Owner promptly and in no event later than 7 Days after the first observance of the conditions. Conditions shall not be disturbed prior to such notice.

B. Adjustment in Contract Time and Contract Sum: If such conditions differ materially and cause a change in Contractor's cost of, or time required for, performance of any part of the Work, the Contractor may be entitled to an equitable adjustment in the Contract Time or Contract Sum, or both, provided it makes a request therefore as provided in Part 7.

5.11 PROTECTION OF EXISTING STRUCTURES, EQUIPMENT, VEGETATION, UTILITIES AND IMPROVEMENTS

A. Contractor to protect and repair property: Contractor shall protect from damage all existing structures, equipment, improvements, utilities, and vegetation: at or near the Project site; and on adjacent property of a third party, the locations of which are made known to or should be known by Contractor. Contractor shall repair any damage, including that to the property of a third party, resulting from failure to comply with the requirements of the Contract Documents or failure to exercise reasonable care in performing the Work. If Contractor fails or refuses to repair the damage promptly, Owner may have the necessary work performed and charge the cost to Contractor.

B. Tree and vegetation protection: Contractor shall only remove trees when specifically authorized to do so, and shall protect vegetation that will remain in place.

5.12 LAYOUT OF WORK

A. Advanced planning of the Work: Contractor shall plan and lay out the Work in advance of operations so as to coordinate all work without delay or revision.

B. Layout responsibilities: Contractor shall lay out the Work from Owner-established baselines and bench marks indicated on the Drawings, and shall be responsible for all field measurements in connection with the layout. Contractor shall furnish, at its own expense, all stakes, templates, platforms, equipment, tools, materials, and labor required to lay out any part of the Work. Contractor shall be responsible for executing the Work to the lines and grades that may be established. Contractor shall be responsible for maintaining or restoring all stakes and other marks established.

5.13 MATERIAL AND EQUIPMENT

A. Contractor to provide new and equivalent equipment and materials: All equipment, material, and articles incorporated into the Work shall be new and of the most suitable grade for the purpose intended, unless otherwise specifically provided in the Contract Documents. References in the Specifications to equipment, material, articles, or patented processes by trade name, make, or catalog number, shall be regarded as establishing a standard quality and shall not be construed as limiting competition. Contractor may, at its option, use any equipment, material, article, or process that, in the judgment of A/E, is equal to that named in the specifications, unless otherwise specifically provided in the Contract Documents.

B. Contractor responsible for fitting parts together: Contractor shall do all cutting, fitting, or patching that may be required to make its several parts fit together properly, or receive or be received by work of others set forth in, or reasonably implied by, the Contract Documents. Contractor shall not endanger any work by cutting, excavating, or otherwise altering the Work and shall not cut or alter the work of any other contractor unless approved in advance by Owner.

C. Owner may reject defective Work: Should any of the Work be found defective, or in any way not in accordance with the Contract Documents, this work, in whatever stage of completion, may be rejected by Owner.

5.14 AVAILABILITY AND USE OF UTILITY SERVICES

A. Owner to provide and charge for utilities: Owner shall make all reasonable utilities available to Contractor from existing outlets and supplies, as specified in the Contract Documents. Unless otherwise provided in the Contract Documents, the utility service consumed shall be charged to or paid for by Contractor at prevailing rates charged to Owner or, where the utility is produced by Owner, at reasonable rates determined by Owner. Contractor will carefully conserve any utilities furnished.

B. Contractor to install temporary connections and meters: Contractor shall, at its expense and in a skillful manner satisfactory to Owner, install and maintain all necessary temporary connections and distribution lines, together with appropriate protective devices, and all meters required to measure the amount of each utility used for the purpose of determining charges. Prior to the date of Final Acceptance, Contractor shall remove all temporary connections, distribution lines, meters, and associated equipment and materials.

5.15 TESTS AND INSPECTION

A. Contractor to provide for all testing and inspection of Work: Contractor shall maintain an adequate testing and inspection program and perform such tests and inspections as are necessary or required to ensure that the Work conforms to the requirements of the Contract Documents. Contractor shall be responsible for inspection and quality surveillance of all its Work and all Work performed by any Subcontractor. Unless otherwise provided, Contractor shall make arrangements for such tests, inspections, and approvals with an independent testing laboratory or entity acceptable to Owner, or with the appropriate public authority, and shall bear all related costs of tests, inspections, and approvals. Contractor shall give Owner timely notice of when and

where tests and inspections are to be made. Contractor shall maintain complete inspection records and make them available to Owner.

B. Owner may conduct tests and inspections: Owner may, at any reasonable time, conduct such inspections and tests as it deems necessary to ensure that the Work is in accordance with the Contract Documents. Owner shall promptly notify Contractor if an inspection or test reveals that the Work is not in accordance with the Contract Documents. Unless the subject items are expressly accepted by Owner, such Owner inspection and tests are for the sole benefit of Owner and do not:

1. Constitute or imply acceptance;

2. Relieve Contractor of responsibility for providing adequate quality control measures;

3. Relieve Contractor of responsibility for risk of loss or damage to the Work, materials, or equipment;

4. Relieve Contractor of its responsibility to comply with the requirements of the Contract Documents; or

5. Impair Owner's right to reject defective or nonconforming items, or to avail itself of any other remedy to which it may be entitled.

C. Inspections or inspectors do not modify Contract Documents: Neither observations by an inspector retained by Owner, the presence or absence of such inspector on the site, nor inspections, tests, or approvals by others, shall relieve Contractor from any requirement of the Contract Documents, nor is any such inspector authorized to change any term or condition of the Contract Documents.

D. Contractor responsibilities on inspections: Contractor shall promptly furnish, without additional charge, all facilities, labor, material and equipment reasonably needed for performing such safe and convenient inspections and tests as may be required by Owner. Owner may charge Contractor any additional cost of inspection or testing when Work is not ready at the time specified by Contractor for inspection or testing, or when prior rejection makes re-inspection or retest necessary. Owner shall perform its inspections and tests in a manner that will cause no undue delay in the Work.

5.16 CORRECTION OF NONCONFORMING WORK

A. Work covered by Contractor without inspection: If a portion of the Work is covered contrary to the requirements in the Contract Documents, it must, if required in writing by Owner, be uncovered for Owner's observation and be replaced at the Contractor's expense and without change in the Contract Time.

B. Payment provisions for uncovering covered Work: If, at any time prior to Final Completion, Owner desires to examine the Work, or any portion of it, which has been covered, Owner may request to see such Work and it shall be uncovered by Contractor. If such Work is in accordance with the Contract Documents, the Contractor shall be entitled to an adjustment in the Contract Sum for the costs of uncovering and replacement, and, if completion of the Work is thereby delayed, an adjustment in the Contract Time, provided it makes such a request as provided in Part 7. If such Work is not in accordance with the Contract Documents, the Contractor shall pay the costs of examination and reconstruction.

C. Contractor to correct and pay for non-conforming Work: Contractor shall promptly correct Work found by Owner not to conform to the requirements of the Contract Documents, whether observed before or after Substantial Completion and whether or not fabricated, installed, or

completed. Contractor shall bear all costs of correcting such nonconforming Work, including additional testing and inspections.

D. Contractor's compliance with warranty provisions: If, within one year after the date of Substantial Completion of the Work or designated portion thereof, or within one year after the date for commencement of any system warranties established under Section 6.08, or within the terms of any applicable special warranty required by the Contract Documents, any of the Work is found to be not in accordance with the requirements of the Contract Documents, Contractor shall correct it promptly after receipt of written notice from Owner to do so. Owner shall give such notice promptly after discovery of the condition. This period of one year shall be extended, with respect to portions of Work first performed after Substantial Completion, by the period of time between Substantial Completion and the actual performance of the Work. Contractor's duty to correct with respect to Work repaired or replaced shall run for one year from the date of repair or replacement. Obligations under this paragraph shall survive Final Acceptance.

E. Contractor to remove non-conforming Work: Contractor shall remove from the Project site portions of the Work which are not in accordance with the requirements of the Contract Documents and are neither corrected by Contractor nor accepted by Owner.

F. Owner may charge Contractor for non-conforming Work: If Contractor fails to correct nonconforming Work within a reasonable time after written notice to do so, Owner may replace, correct, or remove the nonconforming Work and charge the cost thereof to the Contractor.

G. Contractor to pay for damaged Work during correction: Contractor shall bear the cost of correcting destroyed or damaged Work, whether completed or partially completed, caused by Contractor's correction or removal of Work which is not in accordance with the requirements of the Contract Documents.

H. No Period of limitation on other requirements: Nothing contained in this section shall be construed to establish a period of limitation with respect to other obligations which Contractor might have according to the Contract Documents. Establishment of the time period of one year as described in Section 5.16D relates only to the specific obligation of Contractor to correct the Work, and has no relationship to the time within which the Contractor's obligation to comply with the Contract Documents may be sought to be enforced, including the time within which such proceedings may be commenced.

I. Owner may accept non-conforming Work and charge Contractor: If Owner prefers to accept Work which is not in accordance with the requirements of the Contract Documents, Owner may do so instead of requiring its removal and correction, in which case the Contract Sum may be reduced as appropriate and equitable.

5.17 CLEAN UP

Contractor to keep site clean and leave it clean: Contractor shall at all times keep the Project site, including hauling routes, infrastructures, utilities, and storage areas, free from accumulations of waste materials. Before completing the Work, Contractor shall remove from the premises its rubbish, tools, scaffolding, equipment, and materials. Upon completing the Work, Contractor shall leave the Project site in a clean, neat, and orderly condition satisfactory to Owner. If Contractor fails to clean up as provided herein, and after reasonable notice from Owner, Owner may do so and the cost thereof shall be charged to Contractor.

5.18 ACCESS TO WORK

Owner and A/E access to Work site: Contractor shall provide Owner and A/E access to the Work in progress wherever located.

5.19 OTHER CONTRACTS

Owner may award other contracts; Contractor to cooperate: Owner may undertake or award other contracts for additional work at or near the Project site. Contractor shall reasonably cooperate with the other contractors and with Owner's employees and shall carefully adapt scheduling and perform the Work in accordance with these Contract Documents to reasonably accommodate the other work.

5.20 SUBCONTRACTORS AND SUPPLIERS

A. Subcontractor Responsibility: The Contractor shall include the language of this paragraph in each of its first tier subcontracts, and shall require each of its subcontractors to include the same language of this section in each of their subcontracts, adjusting only as necessary the terms used for the contracting parties. Upon request of the Owner, the Contractor shall promptly provide documentation to the Owner demonstrating that the subcontractor meets the subcontractor responsibility criteria below. The requirements of this paragraph apply to all subcontractors regardless of tier. At the time of subcontract execution, the Contractor shall verify that each of its first tier subcontractors meets the following bidder responsibility criteria:

1. Have a current certificate of registration as a contractor in compliance with chapter 18.27 RCW, which must have been in effect at the time of subcontract bid submittal;

2. Have a current Washington Unified Business Identifier (UBI) number;

3. If applicable, have:

    a. Industrial Insurance (workers' compensation) coverage for the subcontractor's employees working in Washington, as required in Title 51 RCW;

    b. A Washington Employment Security Department number, as required in Title 50 RCW;

    c. A Washington Department of Revenue state excise tax registration number, as required in Title 82 RCW;

    d. An electrical contractor license, if required by Chapter 19.28 RCW;

    e. An elevator contractor license, if required by Chapter 70.87 RCW.

4. Not be disqualified from bidding on any public works contract under RCW 39.06.010 or 39.12.065 (3).

5. On a project subject to the apprenticeship utilization requirements in RCW 39.04.320, not have been found out of compliance by the Washington state apprenticeship and training council for working apprentices out of ratio, without appropriate supervision, or outside their approved work processes as outlined in their standards of apprenticeship under chapter 49.04 RCW for the one-year period immediately preceding the date of the Owner's first advertisement of the project.

B. Provide names of Subcontractors and use qualified firms: Before submitting the first Application for Payment, Contractor shall furnish in writing to Owner the names, addresses, and telephone numbers of all Subcontractors, as well as suppliers providing materials in excess of $2,500. Contractor shall utilize Subcontractors and suppliers which are experienced and qualified, and meet the requirements of the Contract Documents, if any. Contractor shall not utilize any Subcontractor or supplier to whom the Owner has a reasonable objection, and shall obtain Owner's written consent before making any substitutions or additions.

C. Subcontracts in writing and pass through provision: All Subcontracts must be in writing. By appropriate written agreement, Contractor shall require each Subcontractor, so far as applicable to the Work to be performed by the Subcontractor, to be bound to Contractor by terms of the Contract Documents, and to assume toward Contractor all the obligations and responsibilities which Contractor assumes toward Owner in accordance with the Contract Documents. Each Subcontract shall preserve and protect the rights of Owner in accordance with the Contract Documents with respect to the Work to be performed by the Subcontractor so that subcontracting thereof will not prejudice such rights. Where appropriate, Contractor shall require each Subcontractor to enter into similar agreements with Sub-subcontractors. However, nothing in this paragraph shall be construed to alter the contractual relations between Contractor and its Subcontractors with respect to insurance or bonds.

D. Coordination of Subcontractors; Contractor responsible for Work: Contractor shall schedule, supervise, and coordinate the operations of all Subcontractors. No Subcontracting of any of the Work shall relieve Contractor from its responsibility for the performance of the Work in accordance with the Contract Documents or any other obligations of the Contract Documents.

E. Automatic assignment of subcontracts: Each subcontract agreement for a portion of the Work is hereby assigned by Contractor to Owner provided that:

1. Effective only after termination and Owner approval: The assignment is effective only after termination by Owner for cause pursuant to Section 9.01 and only for those Subcontracts which the Owner accepts by notifying the Subcontractor in writing; and

2. Owner assumes Contractor's responsibilities: After the assignment is effective, Owner will assume all future duties and obligations toward the Subcontractor which the Contractor assumed in the Subcontract.

3. Impact of bond: The assignment is subject to the prior rights of the surety, if any, obligated under any bond provided in accordance with the Contract Documents.

5.21 WARRANTY OF CONSTRUCTION

A. Contractor warranty of Work: In addition to any special warranties provided elsewhere in the Contract Documents, Contractor warrants that all Work conforms to the requirements of the Contract Documents and is free of any defect in equipment, material, or design furnished, or workmanship performed by Contractor.

B. Contractor responsibilities: With respect to all warranties, express or implied, for Work performed or materials furnished according to the Contract Documents, Contractor shall:

1. Obtain warranties: Obtain all warranties that would be given in normal commercial practice;

2. Warranties for benefit of Owner: Require all warranties to be executed, in writing, for the benefit of Owner;

3. Enforcement of warranties: Enforce all warranties for the benefit of Owner, if directed by Owner; and

4. Contractor responsibility for subcontractor warranties: Be responsible to enforce any subcontractor's, manufacturer's, or supplier's warranties should they extend beyond the period specified in the Contract Documents.

C. Warranties beyond Final Acceptance: The obligations under this section shall survive Final Acceptance.

5.22 INDEMNIFICATION

A. Contractor to indemnify Owner: Contractor shall defend, indemnify, and hold Owner and A/E harmless from and against all claims, demands, losses, damages, or costs, including but not limited to damages arising out of bodily injury or death to persons and damage to property, caused by or resulting from:

1. Sole negligence of Contractor: The sole negligence of Contractor or any of its Subcontractors;

2. Concurrent negligence: The concurrent negligence of Contractor, or any Subcontractor, but only to the extent of the negligence of Contractor or such Subcontractor; and

3. Patent infringement: The use of any design, process, or equipment which constitutes an infringement of any United States patent presently issued, or violates any other proprietary interest, including copyright, trademark, and trade secret.

B. Employee action and RCW Title 51: In any action against Owner and any other entity indemnified in accordance with this section, by any employee of Contractor, its Subcontractors, Sub-subcontractors, agents, or anyone directly or indirectly employed by any of them, the indemnification obligation of this section shall not be limited by a limit on the amount or type of damages, compensation, or benefits payable by or for Contractor or any Subcontractor under RCW Title 51, the Industrial Insurance Act, or any other employee benefit acts. In addition, Contractor waives immunity as to Owner and A/E only, in accordance with RCW Title 51.

PART 6 – PAYMENTS AND COMPLETION

6.1 CONTRACT SUM

Owner shall pay Contract Sum: Owner shall pay Contractor the Contract Sum plus state sales tax for performance of the Work, in accordance with the Contract Documents.

6.2 SCHEDULE OF VALUES

Contractor to submit Schedule of Values: Before submitting its first Application for Payment, Contractor shall submit to Owner for approval a breakdown allocating the total Contract Sum to each principal category of work, in such detail as requested by Owner ("Schedule of Values"). The approved Schedule of Values shall include appropriate amounts for demobilization, record drawings, O&M manuals, and any other requirements for Project closeout, and shall be used by Owner as the basis for progress payments. Payment for Work shall be made only for and in accordance with those items included in the Schedule of Values.

6.3 APPLICATION FOR PAYMENT

A. Monthly Application for Payment with substantiation: At monthly intervals, unless determined otherwise by Owner, Contractor shall submit to Owner an itemized Application for Payment for Work completed in accordance with the Contract Documents and the approved Schedule of Values. Each application shall be supported by such substantiating data as Owner may require.

B. Contractor certifies Subcontractors paid: By submitting an Application for Payment, Contractor is certifying that all Subcontractors have been paid, less earned retainage in accordance with RCW 60.28.011, as their interests appeared in the last preceding certificate of payment. By submitting an Application for Payment, Contractor is recertifying that the representations set forth in Section 1.03, are true and correct, to the best of Contractor's knowledge, as of the date of the Application for Payment.

C. Reconciliation of Work with Progress Schedule: At the time it submits an Application for Payment, Contractor shall analyze and reconcile, to the satisfaction of Owner, the actual progress of the Work with the Progress Schedule.

D. Payment for material delivered to site or stored off-site: If authorized by Owner, the Application for Payment may include request for payment for material delivered to the Project site and suitably stored, or for completed preparatory work. Payment may similarly be requested for material stored off the Project site, provided Contractor complies with or furnishes satisfactory evidence of the following:

1. Suitable facility or location: The material will be placed in a facility or location that is structurally sound, dry, lighted and suitable for the materials to be stored;

2. Facility or location within 10 miles of Project: The facility or location is located within a 10-mile radius of the Project. Other locations may be utilized, if approved in writing, by Owner;

3. Facility or location exclusive to Project's materials: Only materials for the Project are stored within the facility or location (or a secure portion of a facility or location set aside for the Project);

4. Insurance provided on materials in facility or location: Contractor furnishes Owner a certificate of insurance extending Contractor's insurance coverage for damage, fire, and theft to cover the full value of all materials stored, or in transit;

5. Facility or location locked and secure: The facility or location (or secure portion thereof) is continuously under lock and key, and only Contractor's authorized personnel shall have access;

6. Owner right of access to facility or location: Owner shall at all times have the right of access in company of Contractor;

7. Contractor assumes total responsibility for stored materials: Contractor and its surety assume total responsibility for the stored materials; and

8. Contractor provides documentation and Notice when materials moved to site: Contractor furnishes to Owner certified lists of materials stored, bills of lading, invoices, and other information as may be required, and shall also furnish Notice to Owner when materials are moved from storage to the Project site.

6.4 PROGRESS PAYMENTS

A. Owner to pay within 30 Days: Owner shall make progress payments, in such amounts as Owner determines are properly due, within 30 Days after receipt of a properly executed Application for Payment. Owner shall notify Contractor in accordance with chapter 39.76 RCW if the Application for Payment does not comply with the requirements of the Contract Documents.

B. Withholding retainage; Options for retainage: Owner shall retain 5% of the amount of each progress payment until 45 Days after Final Acceptance and receipt of all documents required by law or the Contract Documents, including, at Owner's request, consent of surety to release of the retainage. In accordance with chapter 60.28 RCW, Contractor may request that monies reserved be retained in a fund by Owner, deposited by Owner in a bank or savings and loan, or placed in escrow with a bank or trust company to be converted into bonds and securities to be held in escrow with interest to be paid to Contractor. Owner may permit Contractor to provide an appropriate bond in lieu of the retained funds.

C. Title passes to Owner upon payment: Title to all Work and materials covered by a progress payment shall pass to Owner at the time of such payment free and clear of all liens, claims, security interests, and encumbrances. Passage of title shall not, however, relieve Contractor from any of its duties and responsibilities for the Work or materials, or waive any rights of Owner to insist on full compliance by Contractor with the Contract Documents.

D. Interest on unpaid balances: Payments due and unpaid in accordance with the Contract Documents shall bear interest as specified in chapter 39.76 RCW.

6.5 PAYMENTS WITHHELD

A. Owner's right to withhold payment: Owner may withhold or, on account of subsequently discovered evidence, nullify the whole or part of any payment to such extent as may be necessary to protect Owner from loss or damage for reasons including but not limited to:

1. Non-compliant Work: Work not in accordance with the Contract Documents;

2. Remaining Work to cost more than unpaid balance: Reasonable evidence that the Work required by the Contract Documents cannot be completed for the unpaid balance of the Contract Sum;

3. Owner correction or completion Work: Work by Owner to correct defective Work or complete the Work in accordance with Section 5.16;

4. Contractor 's failure to perform: Contractor's failure to perform in accordance with the Contract Documents; or

5. Contractor 's negligent acts or omissions: Cost or liability that may occur to Owner as the result of Contractor's fault or negligent acts or omissions.

B. Owner to notify Contractor of withholding for unsatisfactory performance: In any case where part or all of a payment is going to be withheld for unsatisfactory performance, Owner shall notify Contractor in accordance with chapter 39.76 RCW.

6.6 RETAINAGE AND BOND CLAIM RIGHTS

Chapters 39.08 RCW and 60.28 RCW incorporated by reference: Chapters 39.08 RCW and 60.28 RCW, concerning the rights and responsibilities of Contractor and Owner with regard to the performance and payment bonds and retainage, are made a part of the Contract Documents by reference as though fully set forth herein.

6.7 SUBSTANTIAL COMPLETION

Substantial Completion defined: Substantial Completion is the stage in the progress of the Work (or portion thereof designated and approved by Owner) when the construction is sufficiently complete, in accordance with the Contract Documents, so Owner has full and unrestricted use and benefit of the facilities (or portion thereof designated and approved by Owner) for the use for which it is intended. All Work other than incidental corrective or punch list work shall be completed. Substantial Completion shall not have been achieved if all systems and parts are not functional, if utilities are not connected and operating normally, if all required occupancy permits have not been issued, or if the Work is not accessible by normal vehicular and pedestrian traffic routes. The date Substantial Completion is achieved shall be established in writing by Owner. Contractor may request an early date of Substantial Completion which must be approved by Change Order. Owner's occupancy of the Work or designated portion thereof does not necessarily indicate that Substantial Completion has been achieved.

6.8 PRIOR OCCUPANCY

A. Prior Occupancy defined; Restrictions: Owner may, upon written notice thereof to Contractor, take possession of or use any completed or partially completed portion of the Work ("Prior Occupancy") at any time prior to Substantial Completion. Unless otherwise agreed in writing, Prior Occupancy shall not: be deemed an acceptance of any portion of the Work; accelerate the time for any payment to Contractor; prejudice any rights of Owner provided by any insurance, bond, guaranty, or the Contract Documents; relieve Contractor of the risk of loss or any of the obligations established by the Contract Documents; establish a date for termination or partial termination of the assessment of liquidated damages; or constitute a waiver of claims.

B. Damage; Duty to repair and warranties: Notwithstanding anything in the preceding paragraph, Owner shall be responsible for loss of or damage to the Work resulting from Prior Occupancy. Contractor's one- year duty to repair any system warranties shall begin on building systems activated and used by Owner as agreed in writing by Owner and Contractor.

6.9 FINAL COMPLETION, ACCEPTANCE, AND PAYMENT

A. Final Completion defined: Final Completion shall be achieved when the Work is fully and finally complete in accordance with the Contract Documents. The date Final Completion is achieved shall be established by Owner in writing, but in no case shall constitute Final Acceptance which is a subsequent, separate, and distinct action.

B. Final Acceptance defined: Final Acceptance shall be achieved when the Contractor has completed the requirements of the Contract Documents. The date Final Acceptance is achieved shall be established by Owner in writing. Prior to Final Acceptance, Contractor shall, in addition to all other requirements in the Contract Documents, submit to Owner a written notice of any outstanding disputes or claims between Contractor and any of its Subcontractors, including the amounts and other details thereof. Neither Final Acceptance, nor final payment, shall release Contractor or its sureties from any obligations of these Contract Documents or the payment and performance bonds, or constitute a waiver of any claims by Owner arising from Contractor's failure to perform the Work in accordance with the Contract Documents.

C. Final payment waives Claim rights: Acceptance of final payment by Contractor, or any Subcontractor, shall constitute a waiver and release to Owner of all claims by Contractor, or any such Subcontractor, for an increase in the Contract Sum or the Contract Time, and for every act or omission of Owner relating to or arising out of the Work, except for those Claims made in accordance with the procedures, including the time limits, set forth in Part 8.

PART 7 – CHANGES

7.1 CHANGE IN THE WORK

A. Changes in Work, Contract Sum, and Contract Time by Change Order: Owner may, at any time and without notice to Contractor's surety, order additions, deletions, revisions, or other changes in the Work. These changes in the Work shall be incorporated into the Contract Documents through the execution of Change Orders. If any change in the Work ordered by Owner causes an increase or decrease in the Contract Sum or the Contract Time, an equitable adjustment shall be made as provided in Section 7.02 or 7.03, respectively, and such adjustment(s) shall be incorporated into a Change Order.

B. Owner may request COP from Contractor: If Owner desires to order a change in the Work, it may request a written Change Order Proposal (COP) from Contractor. Contractor shall submit a Change Order Proposal within 14 Days of the request from Owner, or within such other period as mutually agreed. Contractor's Change Order Proposal shall be full compensation for

implementing the proposed change in the Work, including any adjustment in the Contract Sum or Contract Time, and including compensation for all delays in connection with such change in the Work and for any expense or inconvenience, disruption of schedule, or loss of efficiency or productivity occasioned by the change in the Work.

C. COP negotiations: Upon receipt of the Change Order Proposal, or a request for equitable adjustment in the Contract Sum or Contract Time, or both, as provided in Sections 7.02 and 7.03, Owner may accept or reject the proposal, request further documentation, or negotiate acceptable terms with Contractor. Pending agreement on the terms of the Change Order, Owner may direct Contractor to proceed immediately with the Change Order Work. Contractor shall not proceed with any change in the Work until it has obtained Owner's approval. All Work done pursuant to any Owner-directed change in the Work shall be executed in accordance with the Contract Documents.

D. Change Order as full payment and final settlement: If Owner and Contractor reach agreement on the terms of any change in the Work, including any adjustment in the Contract Sum or Contract Time, such agreement shall be incorporated in a Change Order. The Change Order shall constitute full payment and final settlement of all claims for time and for direct, indirect, and consequential costs, including costs of delays, inconvenience, disruption of schedule, or loss of efficiency or productivity, related to any Work either covered or affected by the Change Order, or related to the events giving rise to the request for equitable adjustment.

E. Failure to agree upon terms of Change Order; Final offer and Claims: If Owner and Contractor are unable to reach agreement on the terms of any change in the Work, including any adjustment in the Contract Sum or Contract Time, Contractor may at any time in writing, request a final offer from Owner. Owner shall provide Contractor with its written response within 30 Days of Contractor's request. Owner may also provide Contractor with a final offer at any time. If Contractor rejects the Owner's final offer, or the parties are otherwise unable to reach agreement, Contractor's only remedy shall be to file a Claim as provided in Part 8.

F. Field Authorizations: The Owner may direct the Contractor to proceed with a change in the work through a written Field Authorization (also referred to as a Field Order) when the time required to price and execute a Change Order would impact the Project.

The Field Authorization shall describe and include the following:

1. The scope of work
2. An agreed upon maximum not-to-exceed amount
3. Any estimated change to the Contract Time
4. The method of final cost determination in accordance with the requirements of Part 7 of the General Conditions
5. The supporting cost data to be submitted in accordance with the requirements of Part 7 of the General Conditions

Upon satisfactory submittal by the Contractor and approval by the Owner of supporting cost data, a Change Order will be executed. The Owner will not make payment to the Contractor for Field Authorization work until that work has been incorporated into an executed Change Order.

7.2 CHANGE IN THE CONTRACT SUM

A. General Application

1. Contract Sum changes only by Change Order: The Contract Sum shall only be changed by a Change Order. Contractor shall include any request for a change in the Contract Sum in its Change Order Proposal.

2. Owner fault or negligence as basis for change in Contract Sum: If the cost of Contractor's performance is changed due to the fault or negligence of Owner, or anyone for whose acts Owner is responsible, Contractor shall be entitled to make a request for an equitable adjustment in the Contract Sum in accordance with the following procedure. No change in the Contract Sum shall be allowed to the extent: Contractor's changed cost of performance is due to the fault or negligence of Contractor, or anyone for whose acts Contractor is responsible; the change is concurrently caused by Contractor and Owner; or the change is caused by an act of Force Majeure as defined in Section 3.05.

   (a) Notice and record keeping for equitable adjustment: A request for an equitable adjustment in the Contract Sum shall be based on written notice delivered to Owner within 7 Days of the occurrence of the event giving rise to the request. For purposes of this part, "occurrence" means when Contractor knew, or in its diligent prosecution of the Work should have known, of the event giving rise to the request. If Contractor believes it is entitled to an adjustment in the Contract Sum, Contractor shall immediately notify Owner and begin to keep and maintain complete, accurate, and specific daily records. Contractor shall give Owner access to any such records and, if requested shall promptly furnish copies of such records to Owner.

   (b) Content of notice for equitable adjustment; Failure to comply: Contractor shall not be entitled to any adjustment in the Contract Sum for any occurrence of events or costs that occurred more than 7 Days before Contractor's written notice to Owner. The written notice shall set forth, at a minimum, a description of: the event giving rise to the request for an equitable adjustment in the Contract Sum; the nature of the impacts to Contractor and its Subcontractors of any tier, if any; and to the extent possible the amount of the adjustment in Contract Sum requested. Failure to properly give such written notice shall, to the extent Owner's interests are prejudiced, constitute a waiver of Contractor's right to an equitable adjustment.

   (c) Contractor to provide supplemental information: Within 30 Days of the occurrence of the event giving rise to the request, unless Owner agrees in writing to allow an additional period of time to ascertain more accurate data, Contractor shall supplement the written notice provided in accordance with subparagraph a. above with additional supporting data. Such additional data shall include, at a minimum: the amount of compensation requested, itemized in accordance with the procedure set forth herein; specific facts, circumstances, and analysis that confirms not only that Contractor suffered the damages claimed, but that the damages claimed were actually a result of the act, event, or condition complained of and that the Contract Documents provide entitlement to an equitable adjustment to Contractor for such act, event, or condition; and documentation sufficiently detailed to permit an informed analysis of the request by Owner. When the request for compensation relates to a delay, or other change in Contract Time, Contractor shall demonstrate the impact on the critical path, in accordance with Section 7.03C. Failure to provide such additional information and documentation within the time allowed or within the format required shall, to the extent Owner's interests are prejudiced, constitute a waiver of Contractor's right to an equitable adjustment.

(d) Contractor to proceed with Work as directed: Pending final resolution of any request made in accordance with this paragraph, unless otherwise agreed in writing, Contractor shall proceed diligently with performance of the Work.

(e) Contractor to combine requests for same event together: Any requests by Contractor for an equitable adjustment in the Contract Sum and in the Contract Time that arise out of the same event(s) shall be submitted together.

3. Methods for calculating Change Order amount: The value of any Work covered by a Change Order, or of any request for an equitable adjustment in the Contract Sum, shall be determined by one of the following methods:

   a. Fixed Price: On the basis of a fixed price as determined in paragraph 7.02B.

   b. Unit Prices: By application of unit prices to the quantities of the items involved as determined in paragraph 7.02C.

   c. Time and Materials: On the basis of time and material as determined in paragraph 7.02D.

4. Fixed price method is default; Owner may direct otherwise: When Owner has requested Contractor to submit a Change Order Proposal, Owner may direct Contractor as to which method in subparagraph 3 above to use when submitting its proposal. Otherwise, Contractor shall determine the value of the Work, or of a request for an equitable adjustment, on the basis of the fixed price method.

B. Change Order Pricing – Fixed Price

Procedures: When the fixed price method is used to determine the value of any Work covered by a Change Order, or of a request for an equitable adjustment in the Contract Sum, the following procedures shall apply:

1. Breakdown and itemization of details on COP: Contractor's Change Order Proposal, or request for adjustment in the Contract Sum, shall be accompanied by a complete itemization of the costs, including labor, material, subcontractor costs, and overhead and profit. The costs shall be itemized in the manner set forth below, and shall be submitted on breakdown sheets in a form approved by Owner.

2. Use of industry standards in calculating costs: All costs shall be calculated based upon appropriate industry standard methods of calculating labor, material quantities, and equipment costs.

3. Costs contingent on Owner's actions: If any of Contractor's pricing assumptions are contingent upon anticipated actions of Owner, Contractor shall clearly state them in the proposal or request for an equitable adjustment.

4. Markups on additive and deductive Work: The cost of any additive or deductive changes in the Work shall be calculated as set forth below, except that overhead and profit shall not be included on deductive changes in the Work. Where a change in the Work involves additive and deductive work by the same Contractor or Subcontractor, small tools, overhead, profit, bond and insurance markups will apply to the net difference.

5. Breakdown not required if change less than $1,000: If the total cost of the change in the Work or request for equitable adjustment does not exceed $1,000, Contractor shall not be required to submit a breakdown if the description of the change in the Work or request for equitable adjustment is sufficiently definitive for Owner to determine fair value.

6. Breakdown required if change between $1,000 and $2,500: If the total cost of the change in the Work or request for equitable adjustment is between $1,000 and $2,500, Contractor may submit a breakdown in the following level of detail if the description of the change in the Work or if the request for equitable adjustment is sufficiently definitive to permit the Owner to determine fair value:

   a. lump sum labor;

   b. lump sum material;

   c. lump sum equipment usage;

   d. overhead and profit as set forth below; and

   e. insurance and bond costs as set forth below.

7. Components of increased cost: Any request for adjustment of Contract Sum based upon the fixed price method shall include only the following items:

   a. Craft labor costs: These are the labor costs determined by multiplying the estimated or actual additional number of craft hours needed to perform the change in the Work by the hourly labor costs. Craft hours should cover direct labor, as well as indirect labor due to trade inefficiencies. The hourly costs shall be based on the following:

      (1) Basic wages and benefits: Hourly rates and benefits as stated on the Department of Labor and Industries approved "statement of intent to pay prevailing wages" or a higher amount if approved by the Owner. Direct supervision shall be a reasonable percentage not to exceed 15% of the cost of direct labor. No supervision markup shall be allowed for a working supervisor's hours.

      (2) Worker's insurance: Direct contributions to the state of Washington for industrial insurance; medical aid; and supplemental pension, by the class and rates established by the Department of Labor and Industries.

      (3) Federal insurance: Direct contributions required by the Federal Insurance Compensation Act; Federal Unemployment Tax Act; and the State Unemployment Compensation Act.

      (4) Travel allowance: Travel allowance and/or subsistence, if applicable, not exceeding those allowances established by regional labor union agreements, which are itemized and identified separately.

      (5) Safety: Cost incurred due to the Washington Industrial Safety and Health Act, which shall be a reasonable percentage not to exceed 2% of the sum of the amounts calculated in (1), (2), and (3) above.

   b. Material costs: This is an itemization of the quantity and cost of materials needed to perform the change in the Work. Material costs shall be developed first from actual known costs, second from supplier quotations or if these are not available, from standard industry pricing guides. Material costs shall consider all available discounts. Freight costs, express charges, or special delivery charges, shall be itemized.

c. Equipment costs: This is an itemization of the type of equipment and the estimated or actual length of time the construction equipment appropriate for the Work is or will be used on the change in the Work. Costs will be allowed for construction equipment only if used solely for the changed Work, or for additional rental costs actually incurred by the Contractor. Equipment charges shall be computed on the basis of actual invoice costs or if owned, from the current edition of one of the following sources:

(1) Associated General Contractors Washington State Department of Transportation (AGC WSDOT) Equipment Rental Agreement current edition, on the Contract execution date.

(2) The National Electrical Contractors Association for equipment used on electrical work.

(3) The Mechanical Contractors Association of America for equipment used on mechanical work.

The EquipmentWatch Rental Rate Blue Book shall be used as a basis for establishing rental rates of equipment not listed in the above sources. The maximum rate for standby equipment shall not exceed that shown in the AGC WSDOT Equipment Rental Agreement, current edition on the Contract execution date.

d. Allowance for small tools, expendables & consumable supplies: Small tools consist of tools which cost $250 or less and are normally furnished by the performing contractor. The maximum rate for small tools shall not exceed the following:

(1) 3% for Contractor: For Contractor, 3% of direct labor costs.

(2) 5% for Subcontractors: For Subcontractors, 5% of direct labor costs.

Expendables and consumables supplies directly associated with the change in Work must be itemized.

e. Subcontractor costs: This is defined as payments Contractor makes to Subcontractors for changed Work performed by Subcontractors of any tier. The Subcontractors' cost of Work shall be calculated and itemized in the same manner as prescribed herein for Contractor.

f. Allowance for overhead: This is defined as costs of any kind attributable to direct and indirect delay, acceleration, or impact, added to the total cost to Owner of any change in the Contract Sum. If the Contractor is compensated under Section 7.03D, the amount of such compensation shall be reduced by the amount Contractor is otherwise entitled to under this subsection (f). This allowance shall compensate Contractor for all non-craft labor, temporary construction facilities, field engineering, schedule updating, as-built drawings, home office cost, B&O taxes, office engineering, estimating costs, additional overhead because of extended time, and any other cost incidental to the change in the Work. It shall be strictly limited in all cases to a reasonable amount, mutually acceptable, or if none can be agreed upon to an amount not to exceed the rates below:

(1). Projects less than $3 million: For projects where the Contract Award Amount is under $3 million, the following shall apply:

(a) Contractor markup on Contractor Work: For Contractor, for any Work actually performed by Contractor's own forces, 16% of the first $50,000 of the cost, and 4% of the remaining cost, if any.

(b) Subcontractor markup for Subcontractor Work: For each Subcontractor (including lower tier subcontractors), for any Work actually performed by its own forces, 16% of the first $50,000 of the cost, and 4% of the remaining cost, if any.

(c) Contractor markup for Subcontractor Work: For Contractor, for any work performed by its Subcontractor(s) 6% of the first $50,000 of the amount due each Subcontractor, and 4% of the remaining amount if any.

(d) Subcontractor markup for lower tier Subcontractor Work: For each Subcontractor, for any Work performed by its Subcontractor(s) of any lower tier, 4% of the first $50,000 of the amount due the sub-Subcontractor, and 2% of the remaining amount if any.

(e) Basis of cost applicable for markup: The cost to which overhead is to be applied shall be developed in accordance with Section 7.02B 7a. – e.

(2). Projects more than $3 million: For projects where the Contract Award Amount is equal to or exceeds $3 million, the following shall apply:

(a) Contractor markup on Contractor Work: For Contractor, for any Work actually performed by Contractor's own forces, 12% of the first $50,000 of the cost, and 4% of the remaining cost, if any.

(b) Subcontractor markup for Subcontractor Work: For each Subcontractor (including lower tier subcontractors), for any Work actually performed by its own forces, 12% of the first $50,000 of the cost, and 4% of the remaining cost, if any.

(c) Contractor markup for Subcontractor Work: For Contractor, for any Work performed by its Subcontractor(s), 4% of the first $50,000 of the amount due each Subcontractor, and 2% of the remaining amount if any.

(d) Subcontractor markup for lower tier Subcontractor Work: For each Subcontractor, for any Work performed by its Subcontractor(s) of any lower tier, 4% of the first $50,000 of the amount due the sub-Subcontractor, and 2% of the remaining amount if any.

(e) Basis of cost applicable for markup: The cost to which overhead is to be applied shall be developed in accordance with Section 7.02B 7a. – e.

g. Allowance for profit: Allowance for profit is an amount to be added to the cost of any change in contract sum, but not to the cost of change in Contract Time for which contractor has been compensated pursuant to the conditions set forth in Section 7.03. It shall be limited to a reasonable amount, mutually acceptable, or if none can be agreed upon, to an amount not to exceed the rates below:

(1) Contractor / Subcontractor markup for self-performed Work: For Contractor or Subcontractor of any tier for work performed by their forces, 6% of the cost developed in accordance with Section 7.02B 7a. – e.

(2) Contractor / Subcontractor markup for Work performed at lower tier: For Contractor or Subcontractor of any tier for work performed by a subcontractor of a lower tier, 4% of the subcontract cost developed in accordance with Section 7.02B 7a. – h.

h. Insurance and bond premiums: Cost of change in insurance or bond premium: This is defined as:

(1) Contractor 's liability insurance: The cost of any changes in Contractor's liability insurance arising directly from execution of the Change Order; and

(2) Payment and Performance Bond: The cost of the additional premium for Contractor's bond arising directly from the changed Work.

The cost of any change in insurance or bond premium shall be added after overhead and allowance for profit are calculated in accordance with subparagraph f and g above.

C. Change Order Pricing – Unit Prices

1. Content of Owner authorization: Whenever Owner authorizes Contractor to perform Work on a unit-price basis, Owner's authorization shall clearly state:

a. Scope: Scope of work to be performed;

b. Reimbursement basis: Type of reimbursement including pre-agreed rates for material quantities; and

c. Reimbursement limit: Cost limit of reimbursement.

2. Contractor responsibilities: Contractor shall:

a. Cooperate with Owner and assist in monitoring the Work being performed. As requested by Owner, Contractor shall identify workers assigned to the Change Order Work and areas in which they are working;

b. Leave access as appropriate for quantity measurement; and

c. Not exceed any cost limit(s) without Owner's prior written approval.

3. Cost breakdown consistent with Fixed Price requirements: Contractor shall submit costs in accordance with paragraph 7.02B and satisfy the following requirements:

a. Unit prices must include overhead, profit, bond and insurance premiums: Unit prices shall include reimbursement for all direct and indirect costs of the Work, including overhead, profit, bond, and insurance costs; and

b. Owner verification of quantities: Quantities must be supported by field measurement statements signed by Owner.

D. Change Order Pricing – Time-and-Material Prices

1. Content of Owner authorization: Whenever Owner authorizes Contractor to perform Work on a time-and-material basis, Owner's authorization shall clearly state:

a. Scope: Scope of Work to be performed;

b. Reimbursement basis: Type of reimbursement including pre-agreed rates, if any, for material quantities or labor; and

c. Reimbursement limit: Cost limit of reimbursement.

2. Contractor responsibilities: Contractor shall:

a. Identify workers assigned: Cooperate with Owner and assist in monitoring the Work being performed. As requested by Owner, identify workers assigned to the Change Order Work and areas in which they are working;

b. Provide daily timesheets: Identify on daily time sheets all labor performed in accordance with this authorization. Submit copies of daily time sheets within 2 working days for Owner's review.

c. Allow Owner to measure quantities: Leave access as appropriate for quantity measurement;

d. Perform Work efficiently: Perform all Work in accordance with this section as efficiently as possible; and

e. Not exceed Owner's cost limit: Not exceed any cost limit(s) without Owner's prior written approval.

3. Cost breakdown consistent with Fixed Price requirements: Contractor shall submit costs in accordance with paragraph 7.02B and additional verification supported by:

a. Timesheets: Labor detailed on daily time sheets; and

b. Invoices: Invoices for material.

7.3 CHANGE IN THE CONTRACT TIME

A. COP requests for Contract Time: The Contract Time shall only be changed by a Change Order. Contractor shall include any request for a change in the Contract Time in its Change Order Proposal.

B. Time extension permitted if not Contractor 's fault: If the time of Contractor's performance is changed due to an act of Force Majeure, or due to the fault or negligence of Owner or anyone for whose acts Owner is responsible, Contractor shall be entitled to make a request for an equitable adjustment in the Contract Time in accordance with the following procedure. No adjustment in the Contract Time shall be allowed to the extent Contractor's changed time of performance is due to the fault or negligence of Contractor, or anyone for whose acts Contractor is responsible.

1. Notice and record keeping for Contract Time request: A request for an equitable adjustment in the Contract Time shall be based on written notice delivered within 7 Days of the occurrence of the event giving rise to the request. If Contractor believes it is entitled to adjustment of Contract Time, Contractor shall immediately notify Owner and begin to keep and maintain complete, accurate, and specific daily records. Contractor shall give Owner access to any such record and if requested, shall promptly furnish copies of such record to Owner.

2. Timing and content of Contractor's Notice: Contractor shall not be entitled to an adjustment in the Contract Time for any events that occurred more than 7 Days before Contractor's written notice to Owner. The written notice shall set forth, at a minimum, a description of: the event giving rise to the request for an equitable adjustment in the

Contract Time; the nature of the impacts to Contractor and its Subcontractors of any tier, if any; and to the extent possible the amount of the adjustment in Contract Time requested. Failure to properly give such written notice shall, to the extent Owner's interests are prejudiced, constitute a waiver of Contractor's right to an equitable adjustment.

3. Contractor to provide supplemental information: Within 30 Days of the occurrence of the event giving rise to the request, unless Owner agrees in writing to allow an additional period of time to ascertain more accurate data, Contractor shall supplement the written notice provided in accordance with subparagraph 7.03B.2 with additional supporting data. Such additional data shall include, at a minimum: the amount of delay claimed, itemized in accordance with the procedure set forth herein; specific facts, circumstances, and analysis that confirms not only that Contractor suffered the delay claimed, but that the delay claimed was actually a result of the act, event, or condition complained of, and that the Contract Documents provide entitlement to an equitable adjustment in Contract Time for such act, event, or condition; and supporting documentation sufficiently detailed to permit an informed analysis of the request by Owner. Failure to provide such additional information and documentation within the time allowed or within the format required shall, to the extent Owner's interests are prejudiced, constitute a waiver of Contractor's right to an equitable adjustment.

4. Contractor to proceed with Work as directed: Pending final resolution of any request in accordance with this paragraph, unless otherwise agreed in writing, Contractor shall proceed diligently with performance of the Work.

C. Contractor to demonstrate impact on critical path of schedule: Any change in the Contract Time covered by a Change Order, or based on a request for an equitable adjustment in the Contract Time, shall be limited to the change in the critical path of Contractor's schedule attributable to the change of Work or event(s) giving rise to the request for equitable adjustment. Any Change Order Proposal or request for an adjustment in the Contract Time shall demonstrate the impact on the critical path of the schedule. Contractor shall be responsible for showing clearly on the Progress Schedule that the change or event: had a specific impact on the critical path, and except in case of concurrent delay, was the sole cause of such impact; and could not have been avoided by resequencing of the Work or other reasonable alternatives.

D. Cost of change in Contract Time: Contractor may request compensation for the cost of a change in Contract Time in accordance with this paragraph, 7.03D, subject to the following conditions:

1. Must be solely fault of Owner or A/E: The change in Contract Time shall solely be caused by the fault or negligence of Owner or A/E;

2. Procedures: Contractor shall follow the procedure set forth in paragraph 7.03B;

3. Demonstrate impact on critical path: Contractor shall establish the extent of the change in Contract Time in accordance with paragraph 7.03C; and

4. Limitations on daily costs: The daily cost of any change in Contract Time shall be limited to the items below, less the amount of any change in the Contract Sum the Contractor may otherwise be entitled to pursuant to Section 7.02B 7f for any change in the Work that contributed to this change in Contract Time:

   a. Non-productive supervision or labor: cost of nonproductive field supervision or labor extended because of delay;

   b. Weekly meetings and indirect activities: cost of weekly meetings or similar indirect activities extended because of the delay;

c. Temporary facilities or equipment rental: cost of temporary facilities or equipment rental extended because of the delay;

d. Insurance premiums: cost of insurance extended because of the delay;

e. Overhead: general and administrative overhead in an amount to be agreed upon, but not to exceed 3% of the Contract Award Amount divided by the originally specified Contract Time for each Day of the delay.

PART 8 – CLAIMS AND DISPUTE RESOLUTION

8.1 CLAIMS PROCEDURE

A. Claim is Contractor's remedy: If the parties fail to reach agreement on the terms of any Change Order for Owner-directed Work as provided in Section 7.01, or on the resolution of any request for an equitable adjustment in the Contract Sum as provided in Section 7.02 or the Contract Time as provided in Section 7.03, Contractor's only remedy shall be to file a Claim with Owner as provided in this section.

B. Claim filing deadline for Contractor: Contractor shall file its Claim within 120 Days from Owner's final offer made in accordance with paragraph 7.01E, or by the date of Final Acceptance, whichever occurs first.

C. Claim must cover all costs and be documented: The Claim shall be deemed to cover all changes in cost and time (including direct, indirect, impact, and consequential) to which Contractor may be entitled. It shall be fully substantiated and documented. At a minimum, the Claim shall contain the following information:

1. Factual statement of Claim: A detailed factual statement of the Claim for additional compensation and time, if any, providing all necessary dates, locations, and items of Work affected by the Claim;

2. Dates: The date on which facts arose which gave rise to the Claim;

3. Owner and A/E employee's knowledgeable about Claim: The name of each employee of Owner or A/E knowledgeable about the Claim;

4. Support from Contract Documents: The specific provisions of the Contract Documents which support the Claim;

5. Identification of other supporting information: The identification of any documents and the substance of any oral communications that support the Claim;

6. Copies of supporting documentation: Copies of any identified documents, other than the Contract Documents, that support the Claim;

7. Details on Claim for Contract Time: If an adjustment in the Contract Time is sought: the specific days and dates for which it is sought; the specific reasons Contractor believes an extension in the Contract Time should be granted; and Contractor's analysis of its Progress Schedule to demonstrate the reason for the extension in Contract Time;

8. Details on Claim for adjustment of Contract Sum: If an adjustment in the Contract Sum is sought, the exact amount sought and a breakdown of that amount into the categories set forth in, and in the detail as required by Section 7.02; and

9. Statement certifying Claim: A statement certifying, under penalty of perjury, that the Claim is made in good faith, that the supporting cost and pricing data are true and accurate to the best of Contractor's knowledge and belief, that the Claim is fully supported by the accompanying data, and that the amount requested accurately reflects the adjustment in the Contract Sum or Contract Time for which Contractor believes Owner is liable.

D. Owner's response to Claim filed: After Contractor has submitted a fully documented Claim that complies with all applicable provisions of Parts 7 and 8, Owner shall respond, in writing, to Contractor as follows:

1. Response time for Claim less than $50,000: If the Claim amount is less than $50,000, with a decision within 60 Days from the date the Claim is received; or

2. Response time for Claim of $50,000 or more: If the Claim amount is $50,000 or more, with a decision within 60 Days from the date the Claim is received, or with notice to Contractor of the date by which it will render its decision. Owner will then respond with a written decision in such additional time.

E. Owner's review of Claim and finality of decision: To assist in the review of Contractor's Claim, Owner may visit the Project site, or request additional information, in order to fully evaluate the issues raised by the Claim. Contractor shall proceed with performance of the Work pending final resolution of any Claim. Owner's written decision as set forth above shall be final and conclusive as to all matters set forth in the Claim, unless Contractor follows the procedure set forth in Section 8.02.

F. Waiver of Contractor rights for failure to comply with this Section: Any Claim of the Contractor against the Owner for damages, additional compensation, or additional time, shall be conclusively deemed to have been waived by the Contractor unless made in accordance with the requirements of this Section.

8.2 ARBITRATION

A. Timing of Contractor 's demand for arbitration: If Contractor disagrees with Owner's decision rendered in accordance with paragraph 8.01D, Contractor shall provide Owner with a written demand for arbitration. No demand for arbitration of any such Claim shall be made later than 30 Days after the date of Owner's decision on such Claim; failure to demand arbitration within said 30 Day period shall result in Owner's decision being final and binding upon Contractor and its Subcontractors.

B. Filing of Notice for arbitration: Notice of the demand for arbitration shall be filed with the American Arbitration Association (AAA), with a copy provided to Owner. The parties shall negotiate or mediate under the Voluntary Construction Mediation Rules of the AAA, or mutually acceptable service, before seeking arbitration in accordance with the Construction Industry Arbitration Rules of AAA as follows:

1. Claims less than $30,000: Disputes involving $30,000 or less shall be conducted in accordance with the Northwest Region Expedited Commercial Arbitration Rules; or

2. Claims greater than $30,000: Disputes over $30,000 shall be conducted in accordance with the Construction Industry Arbitration Rules of the AAA, unless the parties agree to use the expedited rules.

C. Arbitration is forum for resolving Claims: All Claims arising out of the Work shall be resolved by arbitration. The judgment upon the arbitration award may be entered, or review of the award may

occur, in the superior court having jurisdiction thereof. No independent legal action relating to or arising from the Work shall be maintained.

D. Owner may combine Claims into same arbitration: Claims between Owner and Contractor, Contractor and its Subcontractors, Contractor and A/E, and Owner and A/E shall, upon demand by Owner, be submitted in the same arbitration or mediation.

E. Settlement outside of arbitration to be documented in Change Order: If the parties resolve the Claim prior to arbitration judgment, the terms of the resolution shall be incorporated in a Change Order. The Change Order shall constitute full payment and final settlement of the Claim, including all claims for time and for direct, indirect, or consequential costs, including costs of delays, inconvenience, disruption of schedule, or loss of efficiency or productivity.

8.3 CLAIMS AUDITS

A. Owner may audit Claims: All Claims filed against Owner shall be subject to audit at any time following the filing of the Claim. Failure of Contractor, or Subcontractors of any tier, to maintain and retain sufficient records to allow Owner to verify all or a portion of the Claim or to permit Owner access to the books and records of Contractor, or Subcontractors of any tier, shall constitute a waiver of the Claim and shall bar any recovery.

B. Contractor to make documents available: In support of Owner audit of any Claim, Contractor shall, upon request, promptly make available to Owner the following documents:

1. Daily time sheets and supervisor's daily reports;
2. Collective bargaining agreements;
3. Insurance, welfare, and benefits records;
4. Payroll registers;
5. Earnings records;
6. Payroll tax forms;
7. Material invoices, requisitions, and delivery confirmations;
8. Material cost distribution worksheet;
9. Equipment records (list of company equipment, rates, etc.);
10. Vendors', rental agencies', Subcontractors', and agents' invoices;
11. Contracts between Contractor and each of its Subcontractors, and all lower-tier Subcontractor contracts and supplier contracts;
12. Subcontractors' and agents' payment certificates;
13. Cancelled checks (payroll and vendors);
14. Job cost report, including monthly totals;
15. Job payroll ledger;
16. Planned resource loading schedules and summaries;

17. General ledger;

18. Cash disbursements journal;

19. Financial statements for all years reflecting the operations on the Work. In addition, the Owner may require, if it deems it appropriate, additional financial statements for 3 years preceding execution of the Work;

20. Depreciation records on all company equipment whether these records are maintained by the company involved, its accountant, or others;

21. If a source other than depreciation records is used to develop costs for Contractor's internal purposes in establishing the actual cost of owning and operating equipment, all such other source documents;

22. All non-privileged documents which relate to each and every Claim together with all documents which support the amount of any adjustment in Contract Sum or Contract Time sought by each Claim;

23. Work sheets or software used to prepare the Claim establishing the cost components for items of the Claim including but not limited to labor, benefits and insurance, materials, equipment, Subcontractors, all documents which establish the time periods, individuals involved, the hours for the individuals, and the rates for the individuals; and

24. Work sheets, software, and all other documents used by Contractor to prepare its bid.

C. Contractor to provide facilities for audit and shall cooperate: The audit may be performed by employees of Owner or a representative of Owner. Contractor, and its Subcontractors, shall provide adequate facilities acceptable to Owner, for the audit during normal business hours. Contractor, and all Subcontractors, shall make a good faith effort to cooperate with Owner's auditors.

PART 9 – TERMINATION OF THE WORK

9.1 TERMINATION BY OWNER FOR CAUSE

A. 7 Day Notice to Terminate for Cause: Owner may, upon 7 Days written notice to Contractor and to its surety, terminate (without prejudice to any right or remedy of Owner) the Work, or any part of it, for cause upon the occurrence of any one or more of the following events:

1. Contractor fails to prosecute Work: Contractor fails to prosecute the Work or any portion thereof with sufficient diligence to ensure Substantial Completion of the Work within the Contract Time;

2. Contractor bankrupt: Contractor is adjudged bankrupt, makes a general assignment for the benefit of its creditors, or a receiver is appointed on account of its insolvency;

3. Contractor fails to correct Work: Contractor fails in a material way to replace or correct Work not in conformance with the Contract Documents;

4. Contractor fails to supply workers or materials: Contractor repeatedly fails to supply skilled workers or proper materials or equipment;

5. Contractor failure to pay Subcontractors or labor: Contractor repeatedly fails to make prompt payment due to Subcontractors or for labor;

6. Contractor violates laws: Contractor materially disregards or fails to comply with laws, ordinances, rules, regulations, or orders of any public authority having jurisdiction; or

7. Contractor in material breach of Contract: Contractor is otherwise in material breach of any provision of the Contract Documents.

B. Owner's actions upon termination: Upon termination, Owner may at its option:

1. Take possession of Project site: Take possession of the Project site and take possession of or use all materials, equipment, tools, and construction equipment and machinery thereon owned by Contractor to maintain the orderly progress of, and to finish, the Work;

2. Accept assignment of Subcontracts: Accept assignment of subcontracts pursuant to Section 5.20; and

3. Finish the Work: Finish the Work by whatever other reasonable method it deems expedient.

C. Surety's role: Owner's rights and duties upon termination are subject to the prior rights and duties of the surety, if any, obligated under any bond provided in accordance with the Contract Documents.

D. Contractor 's required actions: When Owner terminates the Work in accordance with this section, Contractor shall take the actions set forth in paragraph 9.02B, and shall not be entitled to receive further payment until the Work is accepted.

E. Contractor to pay for unfinished Work: If the unpaid balance of the Contract Sum exceeds the cost of finishing the Work, including compensation for A/E's services and expenses made necessary thereby and any other extra costs or damages incurred by Owner in completing the Work, or as a result of Contractor's actions, such excess shall be paid to Contractor. If such costs exceed the unpaid balance, Contractor shall pay the difference to Owner. These obligations for payment shall survive termination.

F. Contractor and Surety still responsible for Work performed: Termination of the Work in accordance with this section shall not relieve Contractor or its surety of any responsibilities for Work performed.

G. Conversion of "Termination for Cause" to "Termination for Convenience": If Owner terminates Contractor for cause and it is later determined that none of the circumstances set forth in paragraph 9.01A exist, then such termination shall be deemed a termination for convenience pursuant to Section 9.02.

9.2 TERMINATION BY OWNER FOR CONVENIENCE

A. Owner Notice of Termination for Convenience: Owner may, upon written notice, terminate (without prejudice to any right or remedy of Owner) the Work, or any part of it, for the convenience of Owner.

B. Contractor response to termination Notice: Unless Owner directs otherwise, after receipt of a written notice of termination for either cause or convenience, Contractor shall promptly:

1. Cease Work: Stop performing Work on the date and as specified in the notice of termination;

2. No further orders or Subcontracts: Place no further orders or subcontracts for materials, equipment, services or facilities, except as may be necessary for completion of such portion of the Work as is not terminated;

3. Cancel orders and Subcontracts: Cancel all orders and subcontracts, upon terms acceptable to Owner, to the extent that they relate to the performance of Work terminated;

4. Assign orders and Subcontracts to Owner: Assign to Owner all of the right, title, and interest of Contractor in all orders and subcontracts;

5. Take action to protect the Work: Take such action as may be necessary or as directed by Owner to preserve and protect the Work, Project site, and any other property related to this Project in the possession of Contractor in which Owner has an interest; and

6. Continue performance not terminated: Continue performance only to the extent not terminated

C. Terms of adjustment in Contract Sum if Contract terminated: If Owner terminates the Work or any portion thereof for convenience, Contractor shall be entitled to make a request for an equitable adjustment for its reasonable direct costs incurred prior to the effective date of the termination, plus reasonable allowance for overhead and profit on Work performed prior to termination, plus the reasonable administrative costs of the termination, but shall not be entitled to any other costs or damages, whatsoever, provided however, the total sum payable upon termination shall not exceed the Contract Sum reduced by prior payments. Contractor shall be required to make its request in accordance with the provisions of Part 7.

D. Owner to determine whether to adjust Contract Time: If Owner terminates the Work or any portion thereof for convenience, the Contract Time shall be adjusted as determined by Owner.

PART 10 – MISCELLANEOUS PROVISIONS

10.1 GOVERNING LAW

Applicable law and venue: The Contract Documents and the rights of the parties herein shall be governed by the laws of the state of Washington. Venue shall be in the county in which Owner's principal place of business is located, unless otherwise specified.

10.2 SUCCESSORS AND ASSIGNS

Bound to successors; Assignment of Contract: Owner and Contractor respectively bind themselves, their partners, successors, assigns, and legal representatives to the other party hereto and to partners, successors, assigns, and legal representatives of such other party in respect to covenants, agreements, and obligations contained in the Contract Documents. Neither party shall assign the Work without written consent of the other, except that Contractor may assign the Work for security purposes, to a bank or lending institution authorized to do business in the state of Washington. If either party attempts to make such an assignment without such consent, that party shall nevertheless remain legally responsible for all obligations set forth in the Contract Documents.

10.3 MEANING OF WORDS

Meaning of words used in Specifications: Unless otherwise stated in the Contract Documents, words which have well-known technical or construction industry meanings are used in the Contract Documents in accordance with such recognized meanings. Reference to standard specifications, manuals, or codes of any technical society, organization, or association, or to the code of any governmental authority,

whether such reference be specific or by implication, shall be to the latest standard specification, manual, or code in effect on the date for submission of bids, except as may be otherwise specifically stated. Wherever in these Drawings and Specifications an article, device, or piece of equipment is referred to in the singular manner, such reference shall apply to as many such articles as are shown on the drawings, or required to complete the installation.

10.4 RIGHTS AND REMEDIES

No waiver of rights: No action or failure to act by Owner or A/E shall constitute a waiver of a right or duty afforded them under the Contract Documents, nor shall action or failure to act constitute approval or an acquiescence in a breach therein, except as may be specifically agreed in writing.

10.5 CONTRACTOR REGISTRATION

Contractor must be registered or licensed: Pursuant to RCW 39.06, Contractor shall be registered or licensed as required by the laws of the State of Washington, including but not limited to RCW 18.27.

10.6 TIME COMPUTATIONS

Computing time: When computing any period of time, the day of the event from which the period of time begins shall not be counted. The last day is counted unless it falls on a weekend or legal holiday, in which event the period runs until the end of the next day that is not a weekend or holiday. When the period of time allowed is less than 7 days, intermediate Saturdays, Sundays, and legal holidays are excluded from the computation.

10.7 RECORDS RETENTION

Six year records retention period: The wage, payroll, and cost records of Contractor, and its Subcontractors, and all records subject to audit in accordance with Section 8.03, shall be retained for a period of not less than 6 years after the date of Final Acceptance.

10.8 THIRD-PARTY AGREEMENTS

No third party relationships created: The Contract Documents shall not be construed to create a contractual relationship of any kind between: A/E and Contractor; Owner and any Subcontractor; or any persons other than Owner and Contractor.

10.9 ANTITRUST ASSIGNMENT

Contractor assigns overcharge amounts to Owner: Owner and Contractor recognize that in actual economic practice, overcharges resulting from antitrust violations are in fact usually borne by the purchaser. Therefore, Contractor hereby assigns to Owner any and all claims for such overcharges as to goods, materials, and equipment purchased in connection with the Work performed in accordance with the Contract Documents, except as to overcharges which result from antitrust violations commencing after the Contract Sum is established and which are not passed on to Owner under a Change Order. Contractor shall put a similar clause in its Subcontracts, and require a similar clause in its sub-Subcontracts, such that all claims for such overcharges on the Work are passed to Owner by Contractor.

10.10 HEADINGS AND CAPTIONS

Headings for convenience only: All headings and captions used in these General Conditions are only for convenience of reference, and shall not be used in any way in connection with the meaning, effect, interpretation, construction, or enforcement of the General Conditions, and do not define the limit or describe the scope or intent of any provision of these General Conditions.

SUPPLEMENTAL CONDITIONS
FOR WASHINGTON STATE FACILITIES CONSTRUCTION

(Paragraphs keyed to the State's General Conditions)

2.2 Replaces Section 2.02 – COVERAGE LIMITS INSURANCE COVERAGE CERTIFICATES

A. Insurance Coverage Certificates

The Contractor shall furnish acceptable proof of insurance coverage on the state of Washington Certificate of Insurance form SF500A, dated 07/02/92 or ACORD form.

B. Required Coverages

1. For a contract less than $100,000.00, the coverage required is:

   a. Comprehensive General Liability Insurance – The Contractor shall at all times during the term of this contract, at its cost and expense, carry and maintain general public liability insurance, including contractual liability, against claims for bodily injury, personal injury, death or property damage occurring or arising out of services provided under this contract. This insurance shall cover claims caused by any act, omission, or negligence of the Contractor or its officers, agents, representatives, assigns or servants. The limits of liability insurance, which may be increased as deemed necessary by the contracting parties, shall be:

Each Occurrence	$1,000,000.00
General Aggregate Limits (other than products – commercial operations)	$1,000,000.00
Products – Commercial Operations Limit	$1,000,000.00
Personal and Advertising Injury Limit	$1,000,000.00
Fire Damage Limit (any one fire)	$50,000.00
Medical Expense Limit (any one person)	$5,000.00

   b. If the contract is for underground utility work, then the Contractor shall provide proof of insurance for that above in the form of Explosion, Collapse and Underground (XCU) coverage.

   c. Employers Liability on an occurrence basis in an amount not less than $1,000,000.00 per occurrence.

2. For contracts over $100,000.00 but less than $5,000,000.00 the contractor shall obtain the coverage limits as listed for contracts below $100,000.00 and General Aggregate and Products – Commercial Operations Limit of not less than $2,000,000.00.

3. Coverage for Comprehensive General Bodily Injury Liability Insurance for a contract over $5,000,000.00 is:

Each Occurrence	$2,000,000.00
General Aggregate Limits (other than products – commercial operations)	$4,000,000.00
Products – Commercial Operations limit	$4,000,000.00
Personal and Advertising Injury Limit	$2,000,000.00
Fire Damage Limit (any one fire)	$50,000.00
Medical Expense Limit (any one Person)	$5,000.00

4. For all Contracts – Automobile Liability: in the event that services delivered pursuant to this contract involve the use of vehicles or the transportation of clients, automobile liability insurance shall be required. If Contractor-owned personal vehicles are used, a Business Automobile Policy covering at a minimum Code 2 "owned autos only" must be secured. If Contractor employee's vehicles are used, the Contractor must also include under the Business Automobile Policy Code 9, coverage for non-owned autos. The minimum limits for automobile liability is: $1,000,000.00 per occurrence, using a combined single limit for bodily injury and property damage.

5. For Contracts for Hazardous Substance Removal (Asbestos Abatement, PCB Abatement, etc.)

   a. In addition to providing insurance coverage for the project as outlined above, the Contractor shall provide Pollution Liability insurance for the hazardous substance removal as follows:

EACH OCCURRENCE	AGGREGATE
$500,000.00	$1,000,000.00

   or $1,000,000.00 each occurrence/aggregate bodily injury and property damage combined single limit.

   1) Insurance certificate must state that the insurer is covering hazardous substance removal.
   2) Should this insurance be secured on a "claims made" basis, the coverage must be continuously maintained for one year following the project's "final completion" through official completion of the project, plus one year following.

   For Contracts where hazardous substance removal is a subcomponent of contracted work, the general contractor shall provide to the Owner a certificate of insurance for coverage as defined in 5a. above. The State of Washington must be listed as an additional insured. This certificate of insurance must be provided to the Owner prior to commencing work.

3.02 Replaces Section 3.02 B – CONSTRUCTION SCHEDULE

B. The Progress Schedule shall be in the form of a Critical Path Method (CPM) logic network or, with the approval of the Owner, a bar chart schedule may be submitted. The scheduling of construction is the responsibility of the Contractor and is included in the contract to assure adequate planning and execution of the work. The schedule will be used to evaluate progress of the work for payment based on the Schedule of Values. The schedule shall show the Contractor's planned order and interdependence of activities, and sequence of work. As a minimum the schedule shall include:

- Date of Notice to Proceed;
- Activities (resources, durations, individual responsible for activity, early starts, late starts, early finishes, late finishes, etc.);
- Utility Shutdowns;
- Interrelationships and dependence of activities;
- Planned vs. actual status for each activity;
- Substantial completion;
- Punch list;
- Final inspection;
- Final completion, and
- Float time

The Schedule Duration shall be based on the Contract Time of Completion listed on the Bid Proposal form. The Owner shall not be obligated to accept any Early Completion Schedule suggested by the Contractor. The Contract Time for Completion shall establish the Schedule Completion Date.

If the Contractor feels that the work can be completed in less than the Specified Contract Time, then the Surplus Time shall be considered Project Float. This Float time shall be shown on the Project Schedule. It shall be available to accommodate changes in the work and unforeseen conditions.

Neither the Contractor nor the Owner have exclusive right to this Float Time. It belongs to the project.

5.02 Replace Section 5.02 B – PERMITS, FEES AND NOTICES

B. The actual cost of the general building permit (only) and the public utility hook-up fees will be a direct reimbursement to the Contractor or paid ***directly to the permitting agency*** *by the Owner.* ***Fees for these permits should not be included by the Contractor in his bid amount***

Add New Section 5.02 D – PERMITS, FEES, AND NOTICES

D. The General Contractor shall submit copies of each valid permit required on the project to the Owner's representative. Nothing in this part shall be construed as imposing a duty upon the Owner or A/E to secure permits.

5.7 Replaces 5.07, Section A – SAFETY PRECAUTIONS

A. In performing this contract, the Contractor shall provide for protecting the lives and health of employees and other persons; preventing damage to property, materials, supplies, and equipment; and avoid work interruptions. For these purposes, the Contractor shall:

1. Follow Washington Industrial Safety and Health Act (WISHA) regional directives and provide a site-specific safety program that will require an accident prevention and hazard analysis plan for the contractor and each subcontractor on the work site. The Contractor shall submit a site-specific safety plan to the Owner's representative prior to the initial scheduled construction meeting.

2. Provide adequate safety devices and measures including, but not limited to, the appropriate safety literature, notice, training, permits, placement and use of barricades, signs, signal lights, ladders, scaffolding, staging, runways, hoist, construction elevators, shoring, temporary lighting, grounded outlets, wiring, hazardous materials, vehicles, construction processes, and equipment required by Chapter 19.27 RCW, State Building Code (Uniform Building, Electrical, Mechanical, Fire, and Plumbing Codes); Chapter 212-12 WAC, Fire Marshal Standards, Chapter 49.17 RCW, WISHA; Chapter 296-155 WAC, Safety Standards for Construction Work; Chapter 296-65 WAC; WISHA Asbestos Standard; WAC 296-62-071, Respirator Standard; WAC 296-62, General Occupation Health Standards, WAC 296-24, General Safety and Health Standards, WAC 296-24, General Safety and Health Standards, Chapter 49.70 RCW, and Right to Know Act.

3. Comply with the State Environmental Policy Act (SEPA), Clean Air Act, Shoreline Management Act, and other applicable federal, state, and local statutes and regulations dealing with the prevention of environmental pollution and the preservation of public natural resources.

4. In the event of inadvertent discovery of archaeological resources such as, but not limited to, human remains, funerary objects, sacred objects, artifacts, or objects of cultural significance, all work will stop. The site in the immediate vicinity of the area of discovery will be secured, and the WAARNG's Cultural Resources Manager or Environmental Programs

Manager will be contacted to determine the appropriate response in accordance with the Standard Operating Procedure outlined in the WAARNG's Integrated Cultural Resources Management Plan.

5. Post all permits, notices, and/or approvals in a conspicuous location at the construction site.

6. Provide any additional measures that the Owner determines to be reasonable and necessary for ensuring a safe environment in areas open to the public. Nothing in this part shall be construed as imposing a duty upon the Owner or A/E to prescribe safety conditions relating to employees, public, or agents of the Contractors.

7. The contractor is responsible to follow the reporting procedure as outlined in Attachment #1, Unified Washington Military Department and National Guard Policy No. 10-03 and Military Department Procedure No. EMS 500-3-01-10, Spill Response and Reporting Procedure, Section 4, Responsibility.

5.20 Replace Paragraph B – SUBCONTRACTORS AND SUPPLIERS

B. Every month for the duration of your contract, submit the following payment information through the DES Diversity Compliance program (B2Gnow) at: https://des.diversitycompliance.com/:

- Payments received by the prime contractor from the Agency
- Payments paid to each subcontractor, including all lower tier subcontractors
- Payments paid to each supplier

For B2Gnow account login or account creation details, please refer to the "*Instructions for Submittal of Contractor Invoice for Payment*" Page 2: http://www.des.wa.gov/services/facilities/Construction/Forms/Pages/Forms.aspx

10.11 Add Part 10.11 – MINORITY AND WOMEN'S BUSINESS ENTERPRISES (MWBE) PARTICIPATION

In Accordance with the legislative findings and policies set forth in Chapter 39.19 RCW the state of Washington encourages participation in all of its contracts by MWBE firms certified by the Office of Minority and Women's Business Enterprises (OMWBE). Participation may be either on a direct basis in response to this solicitation or as a subcontractor to a Bidder. Any affirmative action requirements set forth in federal regulations or statutes

included or referenced in the contract documents will apply. Bidders may contact OMWBE to obtain information on certified firms for potential subcontractors/suppliers.

A. When referred to in this Contract, the terms Minority Business Enterprise (MBE) and Women's Business Enterprise (WBE) will be as defined by OMWBE, WAC 326-02-030.

B. OMWBE has compiled a directory of certified firms. Copies of this directory may be obtained through OMWBE. For information regarding the certification process or the certification status of a particular firm, contact:

   OMWBE, P.O. Box 41160, Olympia, Washington 98504-1160, telephone (360) 664-9750.

C. Eligible MWBEs or M/W firms

   MWBE firms utilized for this project for voluntary MWBE goals may be certified by Washington State OMWBE or self-identified as minority or women owned (M/W firm).

D. MWBE Voluntary Goals

   The Owner has established voluntary goals for MWBE participation for this project. The voluntary goals are set forth in the Advertisement for Bids.

E. If any part of the contract, including the supply of materials and equipment, is anticipated to be subcontracted, then prior to receipt of the first payment, Contractor shall submit, pursuant to Section 5.20 A, a list of all subcontractors/suppliers it intends to use, designate whether any of the subcontractors/suppliers are MWBE firms, indicate the anticipated dollar value of each MWBE subcontract, and provide Tax Identification Number (TIN).

F. If any part of the contract, including the supply of materials and equipment is actually subcontracted during completion of the work, then prior to final acceptance or completion of the contract or as otherwise indicated in the contract documents, the Contractor shall submit a statement of participation indicating what MWBEs were used and the dollar value of their subcontracts.

G. The provisions of this section are not intended to replace or otherwise change the requirements of RCW 39.30.060. If said statute is applicable to this contract, then the failure to comply with RCW 39.30.060 will still

render a bid non-responsive.

H. The Contractor shall maintain, for at least three years after completion of this contract, relevant records and information necessary to document the level of utilization of MWBEs and other businesses as subcontractors and suppliers in this contract, as well as any efforts the Contractor makes to increase the participation of MWBEs as listed in Section I below. The Contractor shall also maintain, for at least three years after completion of this contract, a record of all quotes, bids, estimates, or proposals submitted to the Contractor by all businesses seeking to participate as subcontractors or suppliers in this contract. The state shall have the right to inspect and copy such records. If this contract involves federal funds, Contractor shall comply with all record keeping requirements set forth in any federal rules, regulations or statutes included or referenced in the contract documents.

I. Bidders shall advertise opportunities for subcontractors or suppliers in a manner reasonably designed to provide MWBEs capable of performing the work with timely notice of such opportunities, and all advertisements shall include a provision encouraging participation by MWBE firms. Advertising may be done through general advertisements (e.g. newspapers, journals, etc.) or by soliciting bids directly from MWBEs. Bidders shall provide MWBEs that express interest with adequate and timely information about plans, specifications, and requirements of the contract.

J. Contractors shall not create barriers to open and fair opportunities for all businesses including MWBEs to participate in all State contracts and to obtain or compete for contracts and subcontracts as sources of supplies, equipment, construction and services. In considering offers from and doing business with subcontractors and suppliers, the Contractor shall not discriminate on the basis of race, color, creed, religion, sex, age, nationality, marital status, or the presence of any mental or physical disability in an otherwise qualified disabled person.

K. Any violation of the mandatory requirements of this part of the contract shall be a material breach of contract for which the Contractor may be subject to a requirement of specific performance, or damages and sanctions provided by contract, by RCW 39.19.090, or by other applicable laws.

10.12 MINIMUM LEVELS OF APPRENTICESHIP PARTICIPATION

In accordance with RCW 39.04.320 the State of Washington requires 15% apprenticeship participation for projects estimated to cost one million dollars or more.

A. Apprentice participation, under this contract, may be counted towards the

required percentage (%) only if the apprentices are from an apprenticeship program registered and approved by the Washington State Apprenticeship and Training Council (RCW 49.04 and WAC 296-04).

B. Bidders may contact the Department of Labor and Industries, Specialty Compliance Services Division, Apprenticeship Section, P.O. Box 44530, Olympia, WA 98504-4530 by phone at (360) 902-5320, and e-mail at thum235@lni.wa.gov , to obtain information on available apprenticeship programs.

C. For each project that has apprentice requirements, the contractor shall submit a **"Statement of Apprentice/Journeyman Participation"** on forms provided by the Department of General Administration, with every request for progress payment. The Contractor shall submit consolidated and cumulative data collected by the Contractor and collected from all subcontractors by the Contractor. The data to be collected and submitted includes the following:

1. Contractor name and address
2. Contract number
3. Project name
4. Contract value
5. Reporting period "Notice to Proceed" through "Invoicing Date"
6. Name and registration number of each apprentice
7. Total number of apprentices and labor hours worked by them, categorized by trade or craft.
8. Total number of journeymen and labor hours worked by them, categorized by trade or craft.
9. Cumulative combined total of apprentice and journeymen labor hours.
10. Total percentage of apprentice hours worked

D. No changes to the required percentage (%) of apprentice participation shall be allowed without written approval of the Owner. In any request for the change the Contractor shall clearly demonstrate a good faith effort to comply with the requirements for apprentice participation.

E. Any substantive violation of the mandatory requirements of this part of the contract may be a material breach of the contract by the Contractor. The Owner may withhold payment pursuant to Part 6.05, stop the work for cause pursuant to Part 3.04, and terminate the contract for cause pursuant to Part 9.01.

Unified Washington Military Department and National Guard Policy No. 10-04

Title	Spill Reporting
References	WAC 173-303-145(2)
Cross-Reference Number	Military Department Policy EMS-500-1-05-10
Information Contact	Washington Military Department Environmental Office Building #36, Camp Murray (253) 512-8717
Effective Date	January 1, 2011
Revised	New
Approved By	Timothy J. Lowenberg, Major General The Adjutant General WMD Director

Purpose

The purpose of this policy is to provide a consistent and unified reporting structure for Washington Military Department (WMD) communications with local, state and federal regulators in the event of a spill emergency. A spill emergency is an accidental release or discharge of a known or unknown substance, that by its release poses potential harm to the environment (human, ground, water or air).

Scope

This policy applies to all state and federal civilian employees of the WMD and all members of the Washington National Guard.

Policy

This policy outlines the reporting requirements for any hazardous material spill on Military Department property:

- Life threatening spill emergencies should be reported to emergency services through the 911 system. After a spill-related call is reported to 911, a follow up call must be made to the Joint Operations Center (JOC).

- Non-life threatening spill emergencies must be reported to the JOC upon discovery even as the unit containment and cleanup plans are initiated. The JOC will assure the report is

forwarded to the Environmental Section within the Joint Facilities and Environmental Services as soon as possible. The Environmental Section will assure response efforts and reporting requirements are met.

- Spills that occur on WMD properties located on federal facilities, (e.g. Joint Base Lewis McCord, Yakima Training Center and Fairchild Air Force Base) must also be reported according to that federal facility's spill prevention plan or the base/tenant support agreement. Additional reporting requirements may be specified by the managing WMD division, and may be outlined in a Spill Prevention Countermeasure and Control Plan (SPCCP).

  The JOC is located in Building 17 and can be reached at:
  On Camp Murray: (253) 512-8773
  Externally: (888) 276-4362

The Environmental Program Section of the Joint Facilities and Environmental Services is the point of contact for agency environmental hazardous-materials spill reporting activities to the Department of Ecology. The Environmental Section's phone number: (253) 512-8717.

Responsibilities

The Environmental Program Manager of Joint Facilities and Environmental Services is designated as the agency point of contact for communications with other agencies regarding spill reports.

The JOC is designated as the twenty-four hour-a-day; seven-day-a-week (24/7) response dispatcher for spill incidents and will initiate the WMD procedures for spill response by contacting the Environmental Program Manager or designated spill coordinator within the Environmental Program section. The JOC initiates the primary notification procedure; however there may be secondary notification procedures within different divisions of the WMD.

Emergency Response Notification and Spill Response Flowchart

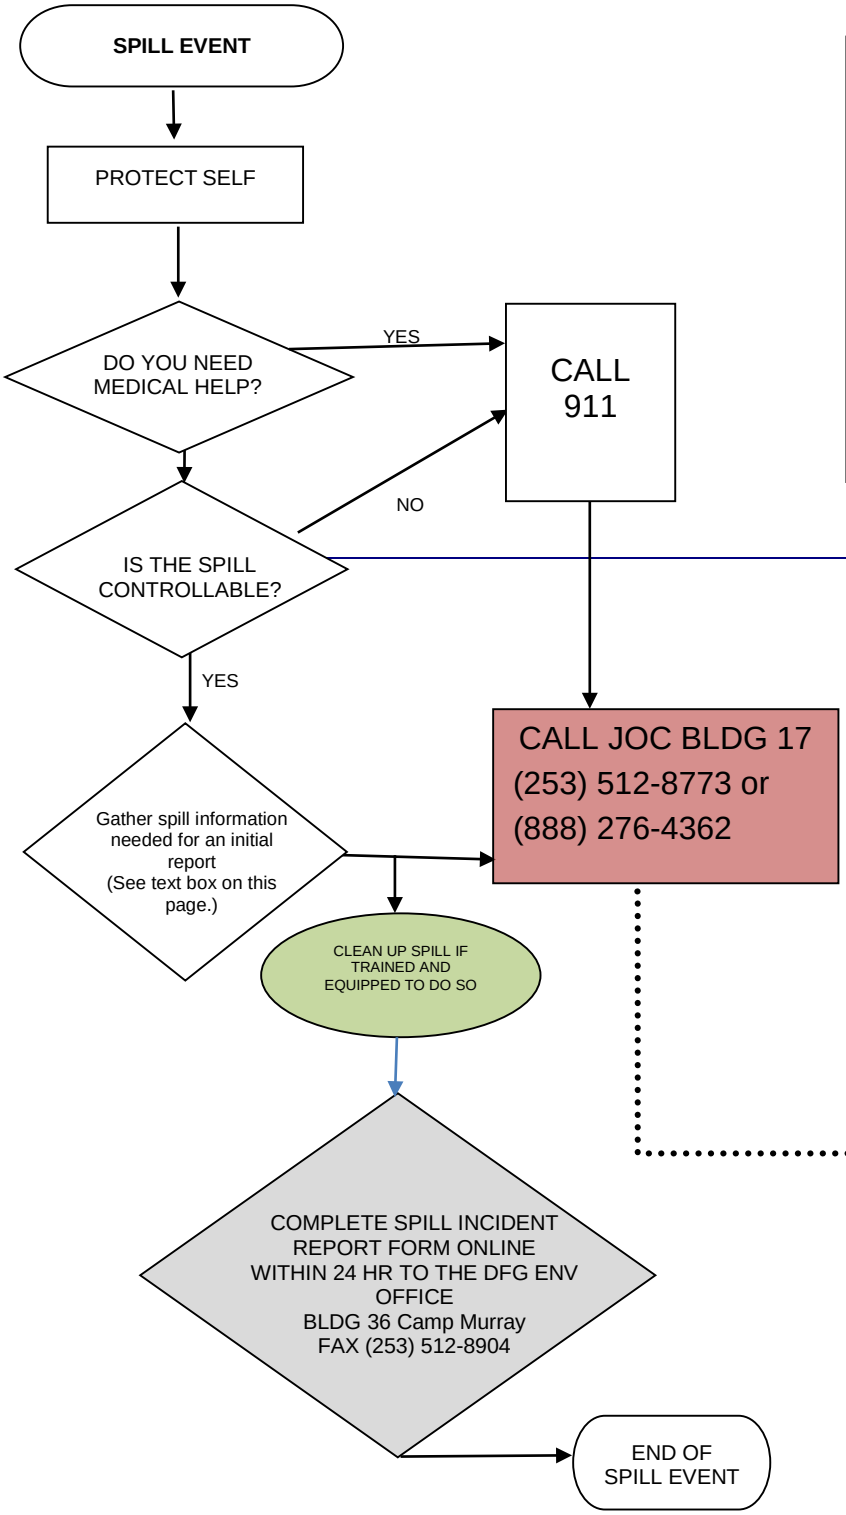

Spill Information Needed for an Initial Report

- Do you know what was spilled?
- Are you able to contain/control/clean-up the spill?
- What is the approximate volume of the spill?
- What was the material spilled on?
- Has the spill reached water or gone down a drain?
- Where is the spill?

Spill Forms Available Online @:

http://milenviro/ems/default.aspx - State Spill Form

https://gkoportal.ngb.army.mil/sites/wang/EMS/default.aspx - Army Spill Form

https://gkoportal2.ngb.army.mil/ang/a7/vemo/campmurray/default.aspx - Air Spill Form

When the Environmental Program Manager cannot be reached the JOC will report every spill event to the Department of Ecology.

Environmental Office
Office: (253) 512-8717
ENV Programs Manager
Office: (253) 512-8466
Cell: (253) 255-8031
HazMat Manager
Office: (253-512-7948
Department of Ecology

NW Region	(425) 649-7000
SW Region	(360) 407-6300
Central Region	(509) 575-2490
Eastern Region	(509) 329-3400

SPILL INCIDENT REPORT

Submit spill report to the Environmental Office after initial cleanup has been completed and within 24 hours. Contact information is at the end of this form.

1. **FACILITY NAME:**_____

   ADDRESS:_____

   CITY or TOWN:_____

   NEAREST HIGHWAY or INTERSECTION:_____

2. **DATE AND TIME OF INCIDENT:**_____

3. **NAME AND TEL. NUMBER OF ON-SCENE CONTACT:**_____

4. **SEVERITY OF THE INCIDENT:** ☐ Spill ☐ Fire ☐ Explosion ☐ Other_____

a. Name or Type of Spilled Material: _____
b. Total Amount Spilled (lbs, gal): _____
c. Amount Recovered (lbs, gal): _____
d. Fate of Recovered Materials (i.e., oil, water, soil, absorbents): _____

☐ Facility Evacuated ☐ Injuries:_____ ☐ Spill Team Activated ☐ Photos

5. **SIGNIFICANT AREAS AFFECTED BY THE SPILL:** (Indicate location of any of the following affected areas, and estimate amount spilled in or on each area). **Affected Area (sq ft):**_____

☐ Building Area ☐ Surface Water
☐ Floor Drains ☐ Storm Drains
☐ Drainage Ditches ☐ Soil or Gravel Surfaces

SPECIFICS
_____
_____

6. **LOCAL TERRAIN CONDITIONS:** (Check off most appropriate description).

☐ Flat: (no significant slope) ☐ Somewhat Flat: (1-5% slope) ☐ Gently Rolling: (5-10% slope)
☐ Sharply Rolling: (10-20% slope) ☐ Steep: (>20% slope)

7. **WEATHER CONDITIONS:** (Check off most appropriate condition).

☐ Dry ☐ Fog or Drizzle ☐ Rain ☐ Snow ☐ Other

8. **CAUSE AND SOURCE OF INCIDENT:** (Check off most appropriate choice and give a brief description of the problem): _____
_____
_____

☐ Equipment Failure ☐ Accident ☐ Human Error ☐ Other

9. **OFFICES NOTIFIED:** (Check-off the offices that were notified and the name of the person who took the report over the telephone).

☐ WAARNG CFMO/ENV Office
☐ Emergency Operations Center
☐ National Response Center

Name: _____
Org: _____
Position: _____
Phone: _____

☐ WA DOE
☐ JOC
☐ Other

Name: _____
Org: _____
Position: _____
Phone: _____

10. **FUTURE PREVENTION:** (Note any equipment repairs or other measures taken to prevent reoccurrence):

_____

_____

Submit this form to the Environmental Office within 24 hours.

Phone: (253) 512-8717 (call for an email address)
Fax: (253) 512-8904

Submit in person at Building 36 on Camp Murray.

Or

For personnel with access to GKO, complete the form online at:
https://states.gkoportal.ng.mil/states/WA/army/NGWA_FMO/NGWA_FMO_ENV/Lists/Spill%20Reporting%20Log/AllItems.aspx

Department of Ecology Report Information

This information is required to be submitted to the Washington State Department of Ecology for any spills or releases:

A. Name, Address, and Phone Number of the owner or operator involved in the incident
B. Name, Address, and Phone Number of the facility or installation involved in the incident
C. Date and Time of the incident
D. Type of incident (Fire, Explosion, Accident, etc.)
E. Name of chemical or material spilled or released
F. Quantity of chemical or material spilled or released (approximate amount)
G. Any injuries (specify type and extent, if known)
H. An assessment of actual hazards or dangers to human health or to the environment
I. An assessment of potential hazards or dangers to human health or to the environment
J. Estimated quantity & disposition of recovered materials (wastes) generated from the incident
K. Cause of the incident
L. Any corrective or preventive actions taken or recommended

Information should be submitted within 15-days and addressed to:

Spills Program Manager (Attention: Dale Jensen) <current as of 10-Jan-2016>
Department of Ecology
P.O. Box 47775
Olympia, WA 98504-775

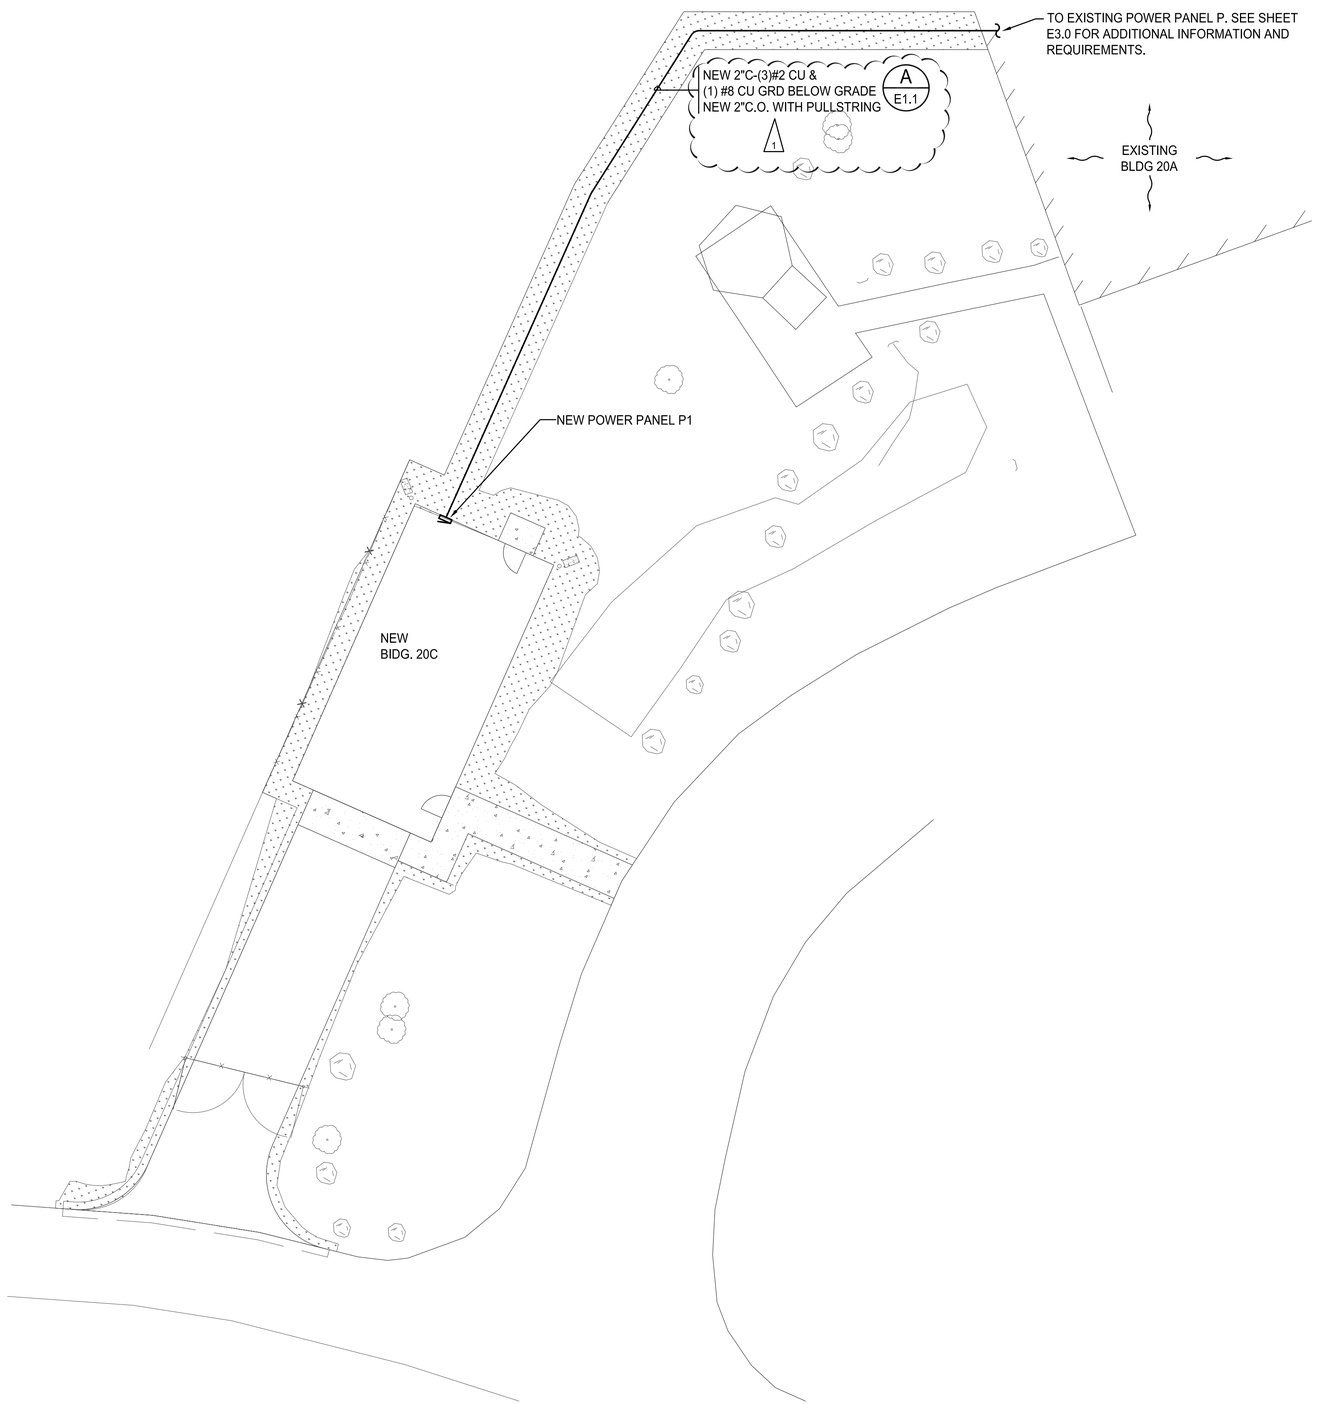

ELECTRICAL SITE PLAN

SCALE: 1"=10'-0"

N

1"=10'-0" GRAPHIC SCALE 10 0 10 20 scale feet

8A

GENERAL NOTES:

1. ELECTRICAL REQUIREMENTS ARE NOT LIMITED TO ELECTRICAL DRAWINGS AND SPECIFICATIONS. THERE IS ADDITIONAL ELECTRICAL WORK REQUIRED TO BE INCLUDED IN THE BID, INDICATED ON ARCHITECTURAL, LANDSCAPE, AND CIVIL DRAWINGS. ADDITIONAL ELECTRICAL WORK REQUIRED IN THE BID IS ALSO LOCATED IN THE SPECIFICATIONS. CONTRACTOR SHALL REVIEW ALL ARCHITECTURAL, CIVIL, AND LANDSCAPE SPECIFICATIONS FOR ADDITIONAL ELECTRICAL INFORMATION AND INCLUDE COSTS FOR THIS IN THE BID.
2. THE CONTRACTOR SHALL BE FULLY RESPONSIBLE FOR THE LOCATION AND PROTECTION OF ALL EXISTING UTILITIES. THE CONTRACTOR SHALL VERIFY ALL UTILITY LOCATIONS PRIOR TO CONSTRUCTION BY CALLING THE UNDERGROUND LOCATE LINE AT 1-(800)-424-5555 A MINIMUM OF 48 HOURS PRIOR TO ANY EXCAVATION. THE CONTRACTOR WILL ALSO BE RESPONSIBLE FOR MAINTAINING ALL LOCATE MARKS ONCE THE UTILITIES HAVE BEEN LOCATED.
3. ALL WALL PENETRATIONS SHALL BE NEATLY CORE-DRILLED, CAULKED AND SEALED TO MAINTAIN FIRE, AND WATERPROOF RATING. PATCH, REPAIR, AND PAINT TO MATCH EXISTING.

ELECTRICAL NOTES:

1. CONTRACTOR SHALL STUB AND CAP 2"C.O. FOR FUTURE COMMUNICATION CABLING NEW EXISTING BUILDING 20A AND IN NEW BUILDING 20C ADJACENT TO NEW POWER PANEL P1. PROVIDE NEW 12"X12"X6", NEMA 3R JUNCTION BOX ON EXTERIOR OF EXISTING BUILDING 20A FOR ROUTING NEW CONDUIT INTO EXISTING BUILDING. CORE DRILL EXISTING EXTERIOR WALL AND STUB/CAP CONDUIT WITHIN BUILDING.

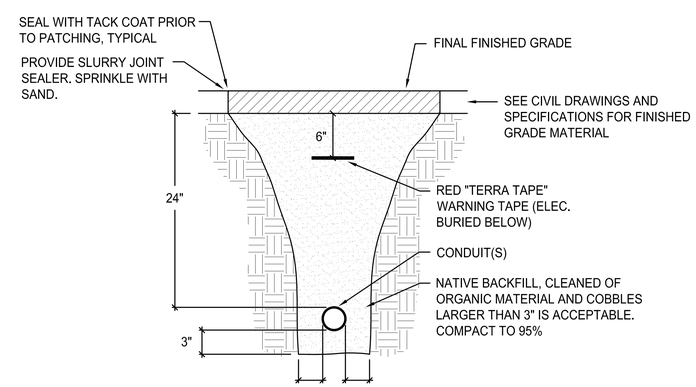

A / E1.1 **TYPICAL CONDUIT TRENCHING**

NOT TO SCALE

BID SET

IF SHEET IS LESS THAN 22" x 34" IT IS A REDUCED SET

CROSS ENGINEERS, INC
6509 6th Avenue
Tacoma, WA 98406
info@crossengineers.com
Phone: (253) 759-0118
Job Number: 16-089

METAL STORAGE BUILDING
20C AVIATION DRIVE
CAMP MURRAY, WASHINGTON

REVISIONS:
1 ADD #1 8-12-16

CONTRACTOR SHALL VERIFY AND COORDINATE THE DIMENSIONS AND DETAILS AMONG ALL DRAWINGS PRIOR TO PROCEEDING WITH THE WORK, AND SHALL NOTIFY THE ARCHITECT OF ANY DISCREPANCIES OR VARIATIONS FROM CONDITIONS SHOWN. DO NOT SCALE DRAWINGS. THESE DRAWINGS ARE THE PROPERTY OF CASTINO ARCHITECTURE. ALL DRAWINGS, DESIGNS AND OTHER INFORMATION ON THE DRAWINGS ARE FOR USE ON THE SPECIFIED PROJECT ONLY, AND SHALL NOT BE USED OTHERWISE WITHOUT THE EXPRESS WRITTEN PERMISSION BY JAMES H. CASTINO, AIA. ARCHITECT ACCEPTS NO LIABILITY AND SHALL BE HELD HARMLESS FROM ANY RESPONSIBILITY FOR DAMAGES RESULTING FROM REVISIONS, CHANGES OR ADAPTATIONS TO THESE DRAWINGS.

STEVEN L. HUBBS
STATE OF WASHINGTON
0029060
REGISTERED
PROFESSIONAL ENGINEER
8/12/16

Castino
Architecture
James Castino
Principal
4810 PT. FOSDICK DR. NW, STE. E-9
Gig HARBOR, WA 98335
PHONE: (253) 851-7648
EMAIL: jimcastino@comcast.net

DATE: AUG. 3, 2016
DRAWN BY: JAE
PROJECT NO.:
FILE NAME:

ELECTRICAL SITE PLAN

SHEET NO:
E1.1

COPYRIGHT 2016
THIS DOCUMENT IS THE PROPERTY OF CASTINO ARCHITECTURE. REPRODUCTION OF ALL OR ANY PORTION OF THIS DOCUMENT WITHOUT WRITTEN PERMISSION IS ILLEGAL AND PUNISHABLE BY LAW.
